

**Project Management Plan
for the
BTev Project**

Fermilab

November 24, 2004

(This page intentionally left blank)

Submitted, Approved, and Accepted By:

BTeV

J. Butler
date

BTeV Project Director

M. Lindgren date
BTeV Project Manager

Fermilab

J. Strait date
Head of Fermilab Particle Physics Division

V. White date
Head of Fermilab Computing Division

R. Dixon date
Head of Fermilab Accelerator Division

R. Kephart date
Head of Fermilab Technical Division

D. Nevin
Head of FESS

W. Griffing date
Head of ES&H Section

H. Montgomery date
Associate Director for Research, Fermilab

S. Holmes date
Associate Director for Accelerators, Fermilab

K. Stanfield date
Deputy Director, Fermilab

M. Witherell
 Director, Fermilab

S. Stone
date

BTeV Collaboration Spokesperson

Department of Energy

R. Lutha
DOE BTeV Project Director

P. Philp date
DOE BTeV Deputy Project Director

Date: _____

(This page intentionally left blank)

BTeV Project Management Plan Change Log

[illegible]

(This page left intentionally blank)

Project Management Plan for the BTeV Project

TABLE OF CONTENTS

1	INTRODUCTION.....	11
1.1	Historical Background	11
1.2	The BTeV Project	11
1.3	Overview of this Document	13
1.4	Revision Control	13
2	JUSTIFICATION OF MISSION	14
2.1	Scientific Objectives	14
2.2	Technical Objectives	14
2.3	Cost Objectives	15
2.4	Schedule Objectives	15
2.5	Project Description	16
2.5.1	<i>C0 Interaction Region</i>	16
2.5.2	<i>C0 Outfitting</i>	16
2.5.3	<i>The BTeV Detector</i>	17
2.5.4	<i>Project Management</i>	18
3	MANAGEMENT, ORGANIZATION, AND RESPONSIBILITIES	20
3.1	Overview	20
3.2	Department of Energy	20
3.3	Fermilab Director	23
3.4	Fermilab Deputy Director	23
3.5	Fermilab Associate Director for Research	23
3.6	Fermilab Particle Physics Division Head	23
3.7	Fermilab Computing Division Head	25
3.8	Fermilab Accelerator Division Head	25
3.9	Fermilab Technical Division Head	27
3.10	Facilities Engineering Services Section Head	28
3.11	Business Services Section Head, Procurement Department Head	29
3.12	BTeV Safety Officer, Fermilab Particle Physics Division Senior Safety Officer and Senior Safety Officers of Beams, Computing, and Technical Divisions	29
3.13	BTeV Spokesperson	30
3.14	BTeV Deputy Spokesperson	31
3.15	BTeV Project Director	31
3.16	BTeV Deputy Project Director	32
3.17	BTeV Project Manager	32
3.18	Technical Coordinators	34

3.19	BTeV Project Subproject Managers	34
3.20	BTeV Collaborator Responsibilities	34
3.21	Advisory Functions	35
3.21.1	<i>BTeV Technical Board</i>	35
3.21.2	<i>BTeV Project Management Group</i>	35
3.21.3	<i>BTeV Executive Committee</i>	35
3.21.4	<i>BTeV International Finance Committee</i>	36
4	WORK BREAKDOWN STRUCTURE.....	37
5	TECHNICAL, SCHEDULE, AND COST BASELINE.....	41
5.1	Technical Baseline and Technical Definition of Project Completion	41
5.2	Project Schedule	41
5.2.1	<i>Schedule Methodology</i>	41
5.2.2	<i>Project Schedule Milestones</i>	42
5.3	Labor Requirements	43
5.4	Project Cost	43
5.4.1	<i>Cost Estimate</i>	43
5.4.2	<i>M&S Contingency Estimation</i>	43
5.5	Cost Summary	44
6	RESOURCE PLAN	44
7	CHANGE CONTROL THRESHOLDS	45
7.1	Change Control Procedures	45
7.2	Technical Change Control Levels	45
7.3	Schedule Change Control Levels	45
7.4	Cost Change Control Levels	46
7.5	Change Control Summary	46
8	RISK MANAGEMENT.....	50
8.1	Risk Management Responsibilities	50
8.2	Types of Risk	51
8.2.1	<i>Technical Risk</i>	51
8.2.2	<i>Cost Risk</i>	51
8.2.3	<i>Schedule Risk</i>	51
8.3	Risk Analysis	52
8.4	Risk Management Tools and Process	52
9	PROJECT CONTROLS SYSTEM	54
9.1	Introduction	54
9.2	Guidelines and Policies	54
9.3	Work Authorization and Contingency Management	55
9.4	Baseline Development	56
9.5	Project Performance Measurement	56
9.5.1	<i>Funds Management</i>	56
9.5.2	<i>Accounting</i>	56

9.5.3 Performance Measurement and Analysis	57
9.5.4 Schedule Variance	57
9.5.5 Cost Variance	57
9.5.6 Resource Variance.....	57
9.6 Change Management	58
9.6.1 Out-of-Scope Changes.....	58
9.6.2 In-Scope Changes	58
9.7 Reporting and Review	58
9.7.1 Monthly Progress Reports.....	58
9.7.2 Technical Design Reports.....	59
9.7.3 Meetings and Reviews	59
10 ACQUISITION STRATEGY	61
10.1 Construction and Fabrication.....	61
10.2 Procurement Plan	61
10.3 Inspection and Acceptance	61
10.4 System Testing and Check out.....	61
11 TECHNICAL CONSIDERATIONS.....	62
12 QUALITY ASSURANCE PROGRAM	62
13 VALUE ENGINEERING.....	64
14 CONFIGURATION MANAGEMENT	64
15 INTEGRATED SAFETY MANAGEMENT	65

(This page left intentionally blank)

1 INTRODUCTION

The BTeV Project Management Plan describes the physics, technical, cost, and schedule objectives for the BTeV Project, which provides the interaction region, supporting experimental facilities and detector for the BTeV experiment, Fermilab Experiment E918. It serves as a supplement to the “DOE Project Execution Plan for the BTeV Project” (the PEP), and provides further details specific to the BTeV Project.

1.1 Historical Background

The High Energy Physics (HEP) program of the Department of Energy (DOE) Office of Science conducts basic research into the nature and interactions of the fundamental constituents of matter. A major component of the US HEP program is the Fermi National Accelerator Laboratory (Fermilab) and its Tevatron Collider. The BTeV experiment will study Rare and CP-violating decays of particles containing bottom quarks and charm quarks in proton-antiproton collisions produced by the Tevatron Collider. The ultimate goal is to discover physics beyond the Standard Model or to help interpret new physics discovered elsewhere by observing its implications in these heavy quark decays.

The BTeV experiment, E918, was first proposed in May of 2000, after several stages of pre-proposal activity and evaluation, and was recommended for approval by the Fermilab Program Advisory Committee (PAC) in June of 2000, a recommendation accepted by the Fermilab Director. In order to reduce the resource requirements of the project in recognition of the evolving DOE/HEP budget realities, the project was de-scoped and resubmitted to Fermilab in its reduced form in April 2002. The PAC again recommended it for approval and the Fermilab Director granted approval. The detector, whose construction is a major part of this project, is the de-scoped version that was approved in April of 2002. The construction of the experiment was endorsed by the Particle Physics Project Prioritization Panel (P5), a subpanel of HEPAP, and their recommendation was adopted by HEPAP on September 30, 2003. The project appears in the Office of Science plan “Facilities for the Future of Science – a Twenty-Year Outlook” as a near-term priority project. The Project was given CD-0 approval in February of 2004.

1.2 The BTeV Project

The purpose of the BTeV Project is to design, construct, and install the BTeV detector, interaction region, and supporting experimental facilities needed to achieve the physics goals set out in the BTeV Proposal Update of April 2002. Beginning in CY 1998, an effort has been underway to carry out conceptual design activities and R&D to be able to construct this detector. This has resulted in a detailed technical design, described in the BTeV Detector Technical Design Report. Parallel efforts to design and specify the components of the Interaction Region, usually referred to as the “IR”, and develop a conceptual design began in 2000. At the same time a project was initiated to design and specify the changes that need to be made in and around the C0 interaction region of the collider to support the BTeV experiment. This activity is referred to as the “C0 Outfitting” Subproject. The implementation of all three of these components, BTeV

detector, C0 Interaction Region and C0 Outfitting is referred to as the “BTev Project” and is the subject of this Project Management Plan.

The principal elements of the BTev Detector sub-project are:

(a) modification and installation of an existing analysis magnet, construction of two toroids (using existing steel), and construction of beam pipes that provide the physical infrastructure of BTev experiment; (b) construction of a silicon pixel vertex detector to reconstruct primary interaction vertices and secondary decay vertices and which can be used in the lowest level trigger of the experiment; (c) construction of a Ring Imaging Cherenkov counter (RICH) to provide charged hadron identification; (d) construction of a high resolution, highly segmented electromagnetic calorimeter to reconstruct photons and π^0 's; (e) construction of a muon detector that can also be used in a stand-alone lowest level trigger; (f) building of a forward tracker based on straw detector technology that covers large angles with respect to the beam and provides tracking in the downstream part of the detector and improves the momentum measurement obtained from the pixel detector alone; (g) building of a forward tracker based on silicon microstrip technology that covers small angles with respect to the beam to provide tracking in the downstream part of the detector; (h) construction of a three level trigger system, including all hardware and software, which is highly efficient for a large variety of bottom and charm decays and achieves excellent rejection of light-quark events; (i) building of a data acquisition system and all necessary interfacing electronics and software to record all events containing a wide variety of bottom and charm decays; and (j) installation in the C0 collision hall, alignment, integration, debugging, and checkout (described below) for all components.

The principal elements of the C0 Interaction Region subproject are:

Construction of a straight section and installation of a wire target station for parasitic testing of BTev detector components as they are completed, and upgrading of the C0 Interaction region to produce high luminosity, 1 to $2 \times 10^{32}/\text{cm}^2\text{-s}$, which will enable BTev to achieve its design sensitivity. This requires the design of a low- β insertion to have collisions at high luminosity in the C0 Interaction Region, to construct the components to implement the design, and to install and commission the components.

The principal elements of the C0 Outfitting subproject are:

Construction of the architectural finishes, mezzanine structures, heating, ventilation, air conditioning (HVAC), process piping systems, and power to support the BTev detector and upgrade of the C0 Service Building, including architectural modification, HVAC and power to support the Interaction Region at C0.

The goal of the complete project is to allow the experimenters, Fermilab, and DOE to meet the scientific objectives described in section 2.1. The timeframe for the Project is to begin construction in FY 2005 and complete the project in FY 2010. Operation of the

full detector will begin in FY2011 but operation with a large portion of the detector, the so-called Stage 1 detector, will occur at the end of calendar 2009.

1.3 Overview of this Document

This document describes the BTeV Project, the project objectives, organization, management, and review mechanisms. The document supplements the PEP by providing additional details specific to the management of the BTeV Project. Section 2 describes the mission justification, including scientific, technical, cost, and schedule objectives. Section 3 describes the Management, Organization, and responsibilities of the various participants. The following 12 sections describe the detailed project objectives, along with a more detailed description of the project, followed by the work plan that will allow us to realize the Project, as well as the resources needed to construct the project. They address the Work Breakdown Structure (section 4), Technical, cost, and schedule baselines (section 5), Resource plan (section 6), change control thresholds (section 7), risk management techniques (section 8), the Project Controls System (section 9), the Acquisition Strategy (section 10), technical considerations (section 11), Quality Assurance (section 12), Value Engineering (section 13), Configuration Management (section 14) and the principles of the Safety Management System (section 15). These are the procedures that will be implemented to assure an on-time and on-budget completion of the project.

1.4 Revision Control

This plan will be reviewed and revised, as required, to reflect new project developments and other agreements among participants. As revisions are issued, they will be signed by the DOE and BTeV signatories and the Fermilab Director and his/her designees. Signatures of other Fermilab officials will be at the discretion of the Fermilab Director. Once signed, the revision will supersede in its entirety previous editions. An entry will be made in the revision log to document the change. A detailed explanation and justification of the change will be placed in the BTeV Document System and announced to all stakeholders.

2 JUSTIFICATION OF MISSION

This section describes the scientific, technical, cost, and schedule objectives that define and justify the mission and goals of the project.

2.1 Scientific Objectives

The purpose of the project is to construct the BTeV detector and install it in the C0 Collision Hall and Counting Room in a state ready to take data and to provide it with a source of high luminosity proton-antiproton collisions in the C0 IR. The detector, a forward spectrometer, covers the forward rapidity region with respect to the antiproton beam. The detector will permit the experimenters to study the decays of produced particles containing b-quarks and charm quarks to search for CP violation, mixing and other rare processes. The ultimate goal is to find physics that is not described by the Standard Model description of these processes and therefore represents “new physics” beyond the Standard Model. The key areas where BTeV excels are in the ability to study decays of the B_s meson and the study decays of B mesons and baryons that contain photons and π^0 's in the final state and to accumulate large statistics samples of B meson and charm meson decays that are almost independent of the final decay products. Achievement of the necessary sensitivity requires modifications to the accelerator to produce high luminosity at the C0 interaction region.

2.2 Technical Objectives

The BTeV Detector must operate successfully in the Tevatron Collider at an instantaneous luminosity of $2 \times 10^{32} \text{ cm}^{-2} \text{ s}^{-1}$ with bunch crossing times of 396 ns.¹ All detector subsystems must be able to withstand the accumulated radiation dose corresponding to an integrated luminosity of 20 fb^{-1} . The detector must be capable of selecting proton-antiproton collision events of interest, in real-time, from the approximately fifteen million collisions per second in the Collider. Detector systems must be sufficiently reliable to assure overall efficiencies of operation of greater than 90%.

To meet the scientific and technical objectives for the BTeV experiment, the following goals must be achieved:

- The Fermilab Tevatron must be modified (mostly in the vicinity of C0) to produce high luminosity, between 1 and $2 \times 10^{32} \text{ cm}^{-2} \text{ s}^{-1}$, at the C0 interaction region in the center of the C0 Collision Hall, where the BTeV detector will be located.
- The Facilities around the C0 Hall and Counting Room must be augmented to support the BTeV Detector and the components of the IR
- The BTeV Detector must be constructed:
 - The BTeV analysis magnet and compensating dipoles, the muon toroids, the beam pipe, and other supporting physical infrastructure must be installed in

¹ The detector should be capable of operating at 264 ns or 132 ns.

C0. All systems must be constructed and installed so as to meet the requirements set forth in the BTeV Technical Design Report.

- The silicon pixel detector, forward straw tracker, forward silicon microstrip tracker, Ring Imaging Cherenkov Counter, Electromagnetic Calorimeter, and Muon Detector and all associated electronics and support systems must be constructed and installed in the C0 interaction region, integrated, and checked out. All systems must be constructed and installed so as to meet the requirements set forth in the BTeV Technical Design Report.
- The trigger system and Event Readout and Control System (data acquisition, a.k.a. DAQ) must be constructed, developed, installed and checked out. All systems must be constructed and installed so as to meet the requirements set forth in the BTeV Technical Design Report.
- All detector subsystems must be integrated with the trigger and data acquisition system.

In order to maximize the data-taking cycle of BTeV, the above systems must be installed and commissioned in an efficient and timely manner. An integrated plan for these activities, under a separate WBS heading, has been developed.

2.3 Cost Objectives

The project cost is summarized Table 7.3 of the PEP. The funding plan for the Project is summarized in Table 6.1 of the PEP and Table 10 of Appendix B of this document. In addition to support from the DOE, funding is being sought through BTeV collaborators both in the United States and abroad, from the National Science Foundation, and the INFN (Italy).

2.4 Schedule Objectives

The primary schedule objectives for the project are summarized in Appendix B Tables 2, 3, 4, and 5. The schedule is based on the DOE schedule in the PEP. In order to meet the challenge of competition from LHCb, BTeV will install key infrastructure components in the C0 Collision Hall in shutdowns projected for installation of accelerator and detector upgrades for Run 2. By taking advantage of shutdown periods, BTeV will then be in a position to carry out parasitic installation of detector components as they are completed. Commissioning using parasitic beam can take place immediately after installation and checkout. The open structure of BTeV facilitates this approach. On the staged schedule proposed by FNAL and BTeV as a result of the CD-1 review, completion of the full detector will occur in two steps: Stage 1 installs most of the capability to study B decays into all-charged final states, about one-half of the electromagnetic calorimeter that enables the study of final states with photons, and about one half of the trigger and data acquisition hardware. This is scheduled for installation in calendar 2009, during the same major shutdown planned to install the C0 interaction region components. After Stage 1 there is an IR commissioning period of one month followed by commissioning of

the Stage 1 detector and a 5 month physics run. In Stage 2, the remaining components of the tracking, particle identification, electromagnetic calorimeter, trigger and data acquisition are installed. Running is scheduled to resume later in 2010 with the full BTeV detector.

2.5 Project Description

The detailed BTeV Project description is provided in the BTeV Technical Design Report. In the following 4 subsections, we describe the main elements of the project. Additional material appears in the description of the Work Breakdown Structure in section 4 below.

2.5.1 C0 Interaction Region

At present, the circulating Tevatron beams do not collide in the C0 region. The Interaction Region Subproject consists of designing the beam optics and designing and constructing the magnets, electrostatic separators, instrumentation, controls, interlocks and supporting systems to focus the two colliding beams at the Interaction Point (IP) and bring them into collision to create high luminosity source of proton-antiproton interactions. All components are in the beam tunnel section outside the C0 Collision Hall, extending 200 m in both directions. A major part of the subproject is the construction of new cryogenic quadrupoles and corrector magnet. As a first step in implementing the IR, the current components in C0 will be removed and replaced by a conventional straight section in a shutdown that will occur in 2005. Preparatory work will also be carried out in C0 during Tevatron shutdowns scheduled for 2006 (if necessary), 2007 and 2008. Installation will take place in the major shutdown scheduled for the summer 2009. The goal is to have the interaction checked out and ready to operate with beam at the end of 2009.

2.5.2 C0 Outfitting

The C0 Collision Hall, Assembly Area, and the accompanying building were constructed in 1999/2000. The C0 area buildings are shells that need to be completed in order to support a complex experiment such as BTeV. In the C0 Assembly Building, the mezzanine will be converted into a three story counting room with facilities adequate to support 24x7 operations. Hardstands for access and parking and gas sheds will be constructed. Power and cooling will be upgraded in the area to support the counting room electronics, detector hall electronics, and the BTeV vertex magnet and toroids. This involves the installation of new substations and pulling a feeder cable from the Kautz Road Substation. The C0 Service Building will be reorganized to support the equipment required to power, monitor and control the components of the C0 IR. Upgrades to AC power in the C1 and D4 service buildings are also required and are part of this subproject.

2.5.3 The BTeV Detector

The BTeV Detector is situated at the C0 interaction region of the Tevatron. It is designed to study the decays of particles containing “b-quarks ” to find “New Physics”, not described by the Standard Model of Particle Physics that would account for the observed matter-antimatter asymmetry of the universe. B decays exhibit the phenomena of “CP Violation”, that is there is a difference between the decays of particle containing “b-quarks” and “b-antiquarks” and can reveal information about this perplexing asymmetry. These goals have been translated into a series of requirements on the detector that are presented in the BTeV Technical Design Report. A brief description is given here. For future reference Work Breakdown Structure numbers are shown in parentheses in the text.

A dipole, the Vertex Magnet (WBS 1.1), centered ON the Interaction Region (IR), gives BTeV a “forward spectrometer” covering the angular range from 10 mr to 300 mr with respect to the direction of the antiproton beam. A large fraction of the B-particles produced at the Tevatron scatter into this region. Inside the dipole, surrounding the interaction region and coming within 6 mm of the beams, there is a precision vertex detector based on planar arrays of silicon pixels, the “pixel detector” (WBS 1.2). This detector is capable of measuring the trajectories of charged particles emerging from the interaction region with sufficient spatial resolution (5-10 μm) to reconstruct primary interaction vertices and “secondary vertices” from B decays, which typically occur between 0.1mm and a few mm from the main interaction. It is the presence of these secondary vertices that distinguish interactions with B decays from the “normal” interactions that occur 500 times more frequently. The bending in the Vertex magnet is observable in the pixel detector and provides a good measurement of the momentum of each charged particle. The pixel detector readout is designed to be fast so the data can be used in the Trigger (WBS 1.8), whose goal is to choose which few hundred events out of the 1.5 million produced by the Tevatron each second contain B decays. By selecting events that are known to have evidence of “secondary vertices” as the “first selection” or “Level 1 trigger”, BTeV is especially efficient for all kinds of B decays.

Once a B particle candidate is “triggered”, its mass must be reconstructed to confirm that it is indeed a B particle and that all its decay products have been contained in the detector, and to determine which of several types of B-particles it is. To reconstruct the mass, one needs the momentum and angles of all the “daughter” particles of the decay and the particle “type” of each daughter. The momentum and angle measurement provided by the pixel detector is improved by measuring the particle trajectories farther down stream of the pixel detector using the “forward tracking system.” This system is composed on 7 stations. Each station has a silicon microstrip detector (WBS 1.7) at small angles and a straw

tube detector (WBS 1.6) at larger angles. The particle identification system, called a Ring Imaging Cherenkov counter (WBS 1.3), determines whether a particle is a pion, kaon, or proton. This information is needed to characterize the decay and to reconstruct the mass.

Several of the most important B decays contain photons in the final state. In order to reconstruct photons, BTeV has a lead tungstate electromagnetic calorimeter (WBS 1.4). This technology, first developed for the CMS detector being built to operate at the LHC, has the excellent energy and spatial resolution and radiation hardness needed by BTeV. With this device, BTeV has excellent ability to reconstruct and study decays of B particles into final states containing photons. The calorimeter also helps identify electrons.

At the end of the system, there is a Muon Detector. It is composed of a toroid magnet (also in WBS 1.1) and proportional tube tracking elements (WBS 1.5). Only muons are able to penetrate the steel of the toroid and record tracks in the proportional tubes. Muons appear as daughter particles in many important B particle decays.

In BTeV, B decays will be collected for several years. The studies that are done are 1) to compare the rates of various decays of B-particle decays and the corresponding decays of the B-antiparticles; 2) to compare various correlations, such as angle correlations between the daughter particles, between B particle decays and B-antiparticle decays; and 3) to compare the “proper time” evolution of the decays of B-particles and antiparticles. The key ingredient of the proper time measurement is the distance between the primary and secondary vertex. The superb spatial resolution of the pixel detector gives BTeV the ability to measure the proper time with great accuracy.

Each detector subsystem has a plan for acquiring parts, testing and assembling various subsystems before transferring to C0. There is an overall installation plan (WBS 1.10) for the entire project. This includes an assembly plan. Common services, such as High Voltage, Low Voltage, and gas, are covered in this part of the project.

Finally, B candidates selected by the trigger must be recorded on an archival medium such as magnetic disk so that they can be studied “offline” and repeatedly mined for physics as new experimental facts and new theoretical ideas emerge. The BTeV Data Acquisition System (WBS 19, formally known as the “event Readout and Control System, and colloquially known as the “DAQ”) accomplishes this.

2.5.4 Project Management

This project is managed by having procedures and roles and responsibilities as defined in this document. Briefly, Level-1 Managers, the Project Director, Deputy Project Director, and Project Manager, are appointed by the laboratory. The Project Director appoints Level-2 managers with the advice of the Project Manager, and in consultation with the collaboration spokesperson. The Project Manager runs the BTeV Project Office that contains the administrative and technical personnel required to support him/her in managing the project. Communication is facilitated by having a variety of meetings, including a weekly meeting of the BTeV Technical Board, Co-chaired by the Project Director and Project Manager, and attended by the leaders of all subprojects and key Project Office Staff. Formal procedures, based on an Earned Value Management System, have been established to ensure that schedules are being met and costs kept under control. Change control procedures are in place, and there is an International Finance Committee to consider the funding needs of the project and identify funding and support from within the collaboration and external to DOE funding provided through Fermilab.

3 MANAGEMENT, ORGANIZATION, AND RESPONSIBILITIES

3.1 Overview

The Project is primarily funded by the DOE and managed through Fermilab. It is carried out in collaboration with universities and laboratories in the US and other countries. Its goal is to construct the BTeV detector and to provide it with collisions to fully exploit the capabilities of the Tevatron to do world class B and charm physics in the LHC era. The Project is to be managed to a predetermined scope, cost and schedule. The responsibilities for managing the project are represented in the organization chart, Fig. 1, and are described in the following sections of this chapter.

3.2 Department of Energy

The Department has established the need for the BTeV Project by considering and responding to advice from its advisory panel, HEPAP, HEPAP's prioritization P5 subpanel, and to Fermilab requests in field task proposals, and by participating in peer review processes for the Fermilab program including the annual DOE laboratory-wide review and the Fermilab Physics Advisory Committee meetings. The BTeV Project appears in the DOE's Office of Science plan "Facilities for the Future of Science – a Twenty-Year Outlook" as a near-term priority project. The Project was given CD-0 approval in February of 2004. The Department of Energy provides the majority of funding for the Project. These funds are provided through the annual Fermilab financial plan by contract modification. The Office of High Energy Physics provides annual program guidance to the laboratory as well as annual guidance on the funding profile for the project. The Department exercises oversight of the Project by:

- conducting periodic reviews of the project;
- participating in regularly scheduled Project Management Group (PMG) meetings;
- overseeing operations and fabrication activities;
- monitoring project progress via monthly reports; and
- monitoring milestones and performance measures.

Support for in-kind contributions are anticipated from INFN, Italy and other funding agencies from the nations of universities and laboratories collaborating on BTeV. Support is also being sought from the US National Science Foundation. The DOE and Fermilab regularly involve the relevant agencies in all the oversight activities described in this document.

The definition of the project, control of its scope, proposals for allocation of project contingency within bounds established in the PEP, oversight and interaction with the collaborating institutions and agencies are the responsibility of the BTeV Project Director. The Project Manager has the responsibility and authority for managing the

project to deliver the approved scope within the total project cost estimate and on schedule. The management structure of the BTeV Project for the DOE is described in detail in the PEP. In particular, the DOE Project Director approves the allocation of contingency, consistent with the PEP.

The following sections relate to management roles of Fermilab management and the relation of the BTeV Collaboration to the project. The DOE oversight of the project is shown in the BTeV PEP.

The portion of the Organization Chart for the BTeV Project at Fermilab is shown in Figure 1. Figure 4.1 of the Project Execution Plan (PEP) shows the DOE management structure that connects to this.

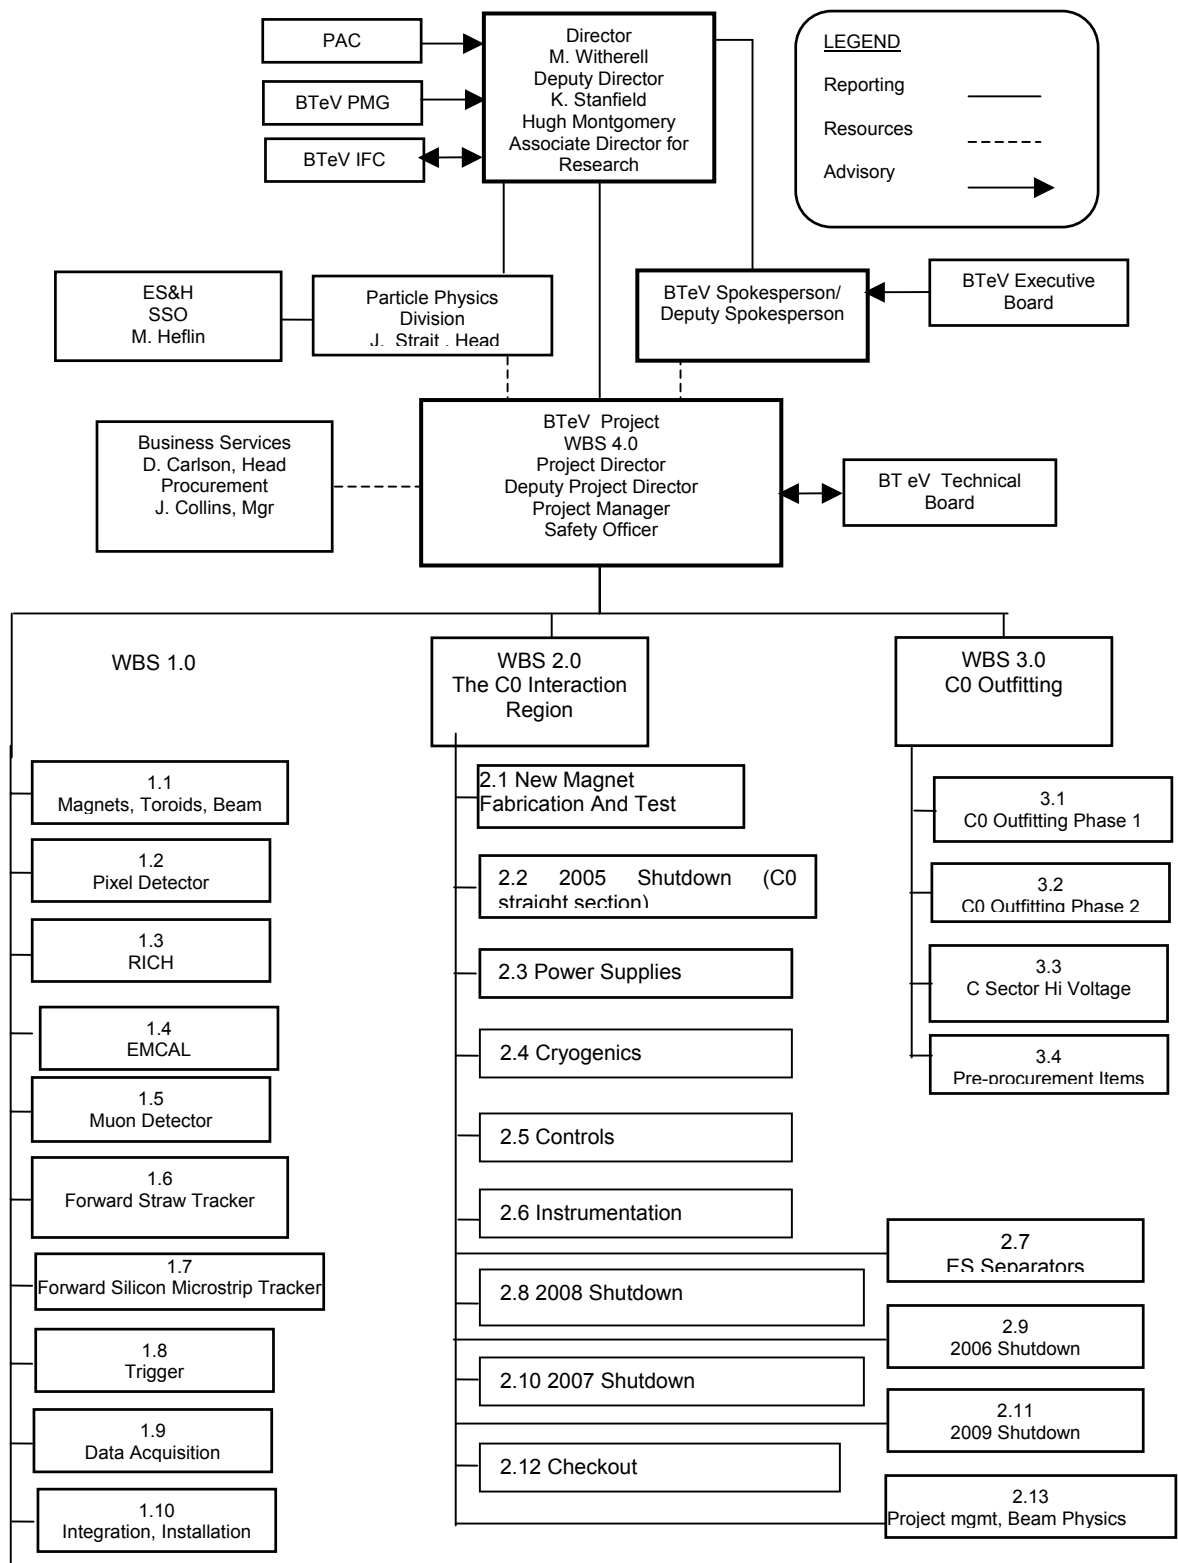


Figure 1 Organization chart for the BTeV Project through WBS Level 2

3.3 Fermilab Director

The Fermilab Director is responsible to the Universities Research Association and the Department of Energy for the successful completion of the BTeV Project and only he/she is authorized to commit funds appropriated for Laboratory use. The Fermilab Director appoints the Fermilab BTeV Project Director, Deputy Project Director, and Project Manager. The Director approves or concurs with the contents of the Technical Design Report (TDR), the Project Management Plan (PMP), the cost estimate, the schedule, the financial plan, and changes in scope for the Project. The Fermilab Director is ultimately responsible for ensuring that the project is carried out safely and with respect for the environment.

3.4 Fermilab Deputy Director

The Director has delegated certain responsibilities and authority to the Deputy Director. The Deputy Director is responsible for Fermilab's management oversight of the Project. Oversight of the Project will be implemented in part through reviews including the Project Management Group (section 3.21.2) and/or Director's Reviews. The Deputy Director chairs the Project Management Group and charges Director's Review panels. Along with routine interactions with project management, these reviews will identify actions and initiatives to be undertaken to achieve the goals of the Project including allocation of financial and human resources. Progress will also be monitored through presentations to and discussions with the PAC. The Deputy Director advises the Director on the approval of the TDR, PMP, cost estimate, schedule, and financial plan and concurs with these approvals. He/she is responsible for providing a funding profile consistent with Laboratory funding after consultation and guidance from the DOE Program Office. The Deputy Director approves or concurs as appropriate with proposals for changes in the cost, schedule, scope or technical baseline of the project.

3.5 Fermilab Associate Director for Research

The Deputy Director has delegated some aspects of BTeV responsibilities to the Associate Director for Research. To implement the work plan for the Project, BTeV Memoranda of Understanding are executed with collaborating institutions. The Associate Director for Research, with the concurrence of the Deputy Director and Director, approves all BTeV Institutional Memoranda of Understanding (MoU) related to the Project. The Associate Director also chairs the International Finance Committee, which coordinates support of the BTeV project by the different funding agencies.

3.6 Fermilab Particle Physics Division Head

The Fermilab Director and Associate Director for Research have delegated certain responsibilities and authorities to the Fermilab Particle Physics Division (PPD) Head. In particular, the Director has designated PPD as the host division for the BTeV Project and as such it provides the resources and home for the BTeV Project management. In addition to the host role, the PPD Head provides oversight for PPD financial resources,

human resources, technical resources, space resources, and Environmental, Safety, and Health (ES&H) monitoring for the Project.

The PPD Head or a designee acceptable to the Laboratory Deputy Director is a member of the Project Management Group. The PPD Head advises the Associate Director for Research on approval of BTeV Memoranda of Understanding relevant to PPD resources and concurs in these approvals. The PPD Head advises the Director and Deputy Director on approval of the PMP and the Cost/Schedule Plan (CSP) and concurs with these approvals .

On guidance from the Director, the PPD Head allocates yearly budgets to the Project. These project funds are then administered by the Project Director and Project Manager, according to the responsibilities described below, within the context of PPD procedures and policies and with the support of the PPD budget office.

The PPD is the primary source of Fermilab manpower and technical resources for the Detector part of the project, as well as the project management activity. The PPD Head and his/her designees may make long-term assignments of PPD manpower directly to the project in consultation with the Project Manager and the Project Director and in accordance with the CSP. The Project Manager then deploys these people to achieve the project goals, reporting changes in assignments to the PPD Head. The PPD Head maintains line management responsibility for these PPD employees.

The PPD also provides support to the BTeV project through its systems and support departments. This is done in accordance with the CSP via specific work plans or BTeV Memoranda of Understanding. The PPD Head maintains direct line management responsibility for such PPD resources.

The BTeV Project is an organizational unit of the PPD. The PPD provides the personnel to staff the BTeV Project Office. The PPD also provides support to the project through PPD technical resource groups. This is done in accordance with the CSP via specific work plans or BTeV Memoranda of Understanding. The PPD Head maintains direct line management responsibility for such PPD resources.

Since the PPD is the primary source for providing the Fermilab labor needed to achieve the project schedule goals for the detector, labor shortfalls must be reported in a timely fashion. The PPD head or designee will advise the Project Manager, Project Director, and Laboratory Deputy Director on the availability and sufficiency of labor resources to meet the project plan as indicated in the CSP. In the event of any mismatch in the availability of labor resources and the requirements, the Project Manager will conduct a schedule impact study and report to the BTeV Project Director, who will consider possible workarounds and propose a schedule variance in the event of a schedule impact to the Laboratory Deputy Director as required by the project controls.

3.7 Fermilab Computing Division Head

The Computing Division is providing a significant fraction of the resources in the area of Trigger (WBS 1.8) and Data Acquisition (WBS 1.9). This responsibility includes both hardware and software.

The CD Head or a designee acceptable to the Laboratory Deputy Director is a member of the Project Management Group. The CD Head advises the Associate Director for Research on approval of BTeV Memoranda of Understanding relevant to CD resources and concurs in these approvals. The CD Head advises the Deputy Director and Associate Director for Research on approval of the PMP and the Cost/Schedule Plan (CSP) and concurs with these approvals.

The CD is the primary source of Fermilab manpower and technical resources for the trigger and data acquisition parts of the project. The CD Head and her/his designees may make long-term assignments of CD personnel directly to the project in consultation with the Project Manager and the Project Director and in accordance with the CSP. The BTeV Project Manager, in consultation with CD representatives and relevant L2 managers, assign CD personnel to achieve the agreed upon scope of work in the CSP. The CD Head maintains line management responsibility for these CD employees.

The CD also provides support to the project through CD technical resource groups. This is done in accordance with the CSP via specific work plans or BTeV Memoranda of Understanding. The CD Head maintains direct line management responsibility for such CD resources.

Since the CD is the primary source for providing the Fermilab labor needed to achieve the project schedule goals in the area of trigger and data acquisition, labor shortfalls must be reported in a timely fashion. The CD head or designee will advise the Project Manager, Project Director, and Laboratory Deputy Director on the availability and sufficiency of labor resources to meet the project plan and report to the BTeV PMG any mismatch in the availability of labor resources and the requirements of the CSP. In the event of any mismatch in the availability of labor resources and the requirements, the Project Manager will conduct a schedule impact study and report to the BTeV Project Director, who will consider possible workarounds and propose a schedule variance as appropriate to the Laboratory Deputy Director as required by the project controls in the event of a schedule impact.

3.8 Fermilab Accelerator Division Head

The Accelerator Division is providing a significant fraction of the resources for the IR subproject, which provides collisions at high luminosity in the C0 IR, WBS 2.0. The AD is responsible for the design of the Interaction Region and for the specification of the required technical components. Some of the technical components will be provided by the Technical Division and others, including power supplies, beam instrumentation, interlocks, and controls and monitoring systems, will be provided by AD. AD is also

responsible for installing the IR, commissioning it, and integrating it into accelerator operations. In addition, the BTeV detector has components that are inside the Tevatron vacuum system and others that closely surround it. Impact on the Tevatron could occur as early as 2005. Moreover, due to the open nature of the detector, partial installation of components is foreseen after about 2006, while CDF and D0 are still taking data. Moreover, the Accelerator Division has a significant role and interest in the C0 Outfitting subproject, both from a design, technical and implementation point of view and from a programmatic point of view (possible interference with operations).

The Accelerator Division Head or a designee acceptable to the Laboratory Deputy Director is a member of the Project Management Group. The Accelerator Division Head advises the Deputy Director on the approval of the BTeV Baseline design as it affects the Tevatron, and on scheduling issues with respect to design, construction, and installation of the C0 IR during the project. It must also advise on BTeV experiment operations in the IR during the project period. The AD Head advises the Deputy Director on approval of BTeV Memoranda of Understanding relevant to AD resources and concurs in these approvals. The AD Head advises the Director and Deputy Director on approval of the PMP and the Cost/Schedule Plan (CSP) and concurs with these approvals.

The Accelerator Division must review and approve BTeV designs that could affect the operation of the Tevatron or its safety, including the baseline design. Once designs are approved, these will constitute an agreement between the BTeV Project and the Accelerator Division to operate the equipment delivered in the agreed upon manner. Reviews must take place on a schedule that is consistent with BTeV Project milestones.

The AD is the primary source of Fermilab manpower and technical resources for the Interaction Region design and installation and is responsible for many of the technical components. The AD Head and her/his designees make long-term assignments of AD personnel directly to the project in consultation with the BTeV Project Manager and the Project Director and in accordance with the CSP. The IR Project manager in consultation with the BTeV Project Manager assigns AD personnel to achieve the agreed upon scope of work in the CSP. The AD Head maintains direct line management responsibility for such AD resources.

The AD also provides support to the BTeV project through its systems and support departments. This is done in accordance with the CSP via specific work plans or BTeV Memoranda of Understanding. The AD Head maintains direct line management responsibility for such AD resources.

Since the AD is one of the primary sources for providing the Fermilab labor needed to achieve the project schedule goals in the area of the C0 IR design and implementation, labor shortfalls must be reported in a timely fashion. The AD head or designee will advise the Project Manager, Project Director, and Laboratory Deputy Director on the availability and sufficiency of labor resources to meet the project plan and report to the BTeV PMG any mismatch in the availability of labor resources and the requirements of

the CSP. In the event of any mismatch in the availability of labor resources and the requirements, the Project Manager will conduct a schedule impact study and report to the BTeV Project Director, who will consider possible workarounds and propose a schedule variance as appropriate to the Laboratory Deputy Director as required by the project controls in the event of a schedule impact.

3.9 Fermilab Technical Division Head

The Technical Division is providing a significant fraction of the resources for the IR subproject, which provides collisions at high luminosity in the C0 IR, WBS 2.0. They are responsible for providing magnets, spool pieces, and other technical components of the IR.

The Technical Division Head or a designee acceptable to the Laboratory Deputy Director is a member of the Project Management Group. The Technical Division Head advises the Deputy Director on the approval of the BTeV Baseline design as it affects the IR and the support of the components it has provided, and on scheduling issues with respect to design, construction, and installation of the C0 IR during the project. The TD Head advises the Deputy Director on approval of BTeV Memoranda of Understanding relevant to TD resources and concurs in these approvals. The TD Head advises the Director and Deputy Director on approval of the PMP and the Cost/Schedule Plan (CSP) and concurs with these approvals.

The TD is the primary source of Fermilab manpower and technical resources for the construction and procurement of Interaction Region design magnets. The TD Head and her/his designees make long-term assignments of TD personnel directly to the project in consultation with the BTeV Project Manager and the Project Director and in accordance with the CSP. The IR Project Manager in consultation with TD representatives and the BTeV Project Manager assigns TD personnel to achieve the agreed upon scope of work in the CSP. The TD Head maintains line management responsibility for these TD employees.

The TD also provides support to the BTeV project through its systems and support departments. This is done in accordance with the CSP via specific work plans or BTeV Memoranda of Understanding. The TD Head maintains direct line management responsibility for such TD resources.

Since the TD is one of the primary sources for providing the Fermilab labor needed to achieve the project schedule goals in the area of the C0 IR design and implementation, labor shortfalls must be reported in a timely fashion. The TD head or designee will advise the Project Manager, Project Director, and Laboratory Deputy Director on the availability and sufficiency of labor resources to meet the project plan and report to the BTeV PMG any mismatch in the availability of labor resources and the requirements of the CSP. In the event of any mismatch in the availability of labor resources and the requirements, the Project Manager will conduct a schedule impact study and report to the BTeV Project Director, who will consider possible workarounds and propose a schedule variance as

appropriate to the Laboratory Deputy Director as required by the project controls in the event of a schedule impact.

3.10 Facilities Engineering Services Section Head

The Facilities Engineering Services Section (FESS) is providing the most of the resources for the C0 Outfitting subproject., WBS 3.0. FESS is responsible for the design work, bid package preparation, contract supervision, inspection and acceptance of the work comprising the C0 Outfitting subproject.

The FESS Head or a designee acceptable to the Laboratory Deputy Director is a member of the Project Management Group. The FESS Section Head advises the Deputy Director on the approval of the BTeV Baseline design as it affects the outfitting of the C0 area and the support of the components it has provided, and on scheduling issues with respect to design, construction, and installation of modifications to the C0 area to support the BTeV experiment. The FESS Head advises the Laboratory Deputy Director on approval of BTeV Memoranda of Understanding relevant to FESS resources and concurs in these approvals. The FESS Head advises the Director and Deputy Director on approval of the PMP and the Cost/Schedule Plan (CSP).

FESS is the primary source of Fermilab manpower and technical resources for the C0 Outfitting subproject. The FESS Head and her/his designees may make long-term assignments of FESS personnel directly to the project in consultation with the BTeV Project Manager and the Project Director and in accordance with the CSP. The Project Manager, in consultation with FESS representatives, then deploys these people to achieve the project goals, reporting changes in assignments to the FESS Head. The FESS Head maintains line management responsibility for these FESS employees.

FESS provides support to the BTeV project through its departments. This is done in accordance with the CSP via specific work plans or BTeV Memoranda of Understanding. The FESS Head maintains direct line management responsibility for such FESS resources.

Since FESS is the primary source for providing the Fermilab labor needed to achieve the project schedule goals in the area of the C0 Outfitting, labor shortfalls or contractor delays and problems must be reported in a timely fashion. The FESS head or designee will advise the Project Manager, Project Director, and Laboratory Deputy Director on the availability and sufficiency of labor resources to meet the project plan and report to the BTeV PMG any mismatch in the availability of labor resources and the requirements of the CSP. In the event of any mismatch in the availability of labor resources and the requirements, the Project Manager will conduct a schedule impact study and report to the BTeV Project Director, who will consider possible workarounds and propose a schedule variance as appropriate to the Laboratory Deputy Director as required by the project controls in the event of a schedule impact.

3.11 Business Services Section Head, Procurement Department Head

Business Services provides support for procurement, financial transactions, and accounting activities necessary to accomplish projects. The Head of Business Services and the Head of the Procurement Department of Business Services will work with BTeV Management to accomplish the large number of procurements on schedule and to meet technical specifications. To this end, the Procurement Department has provided BTeV Management with specific guidance concerning the lead time required to place various kinds of orders. In addition, Business Services has an agreement to support OpenPlan Software from WELCOM Co., which is used by BTeV to produce and status their schedule.

3.12 BTeV Safety Officer, Fermilab Particle Physics Division Senior Safety Officer and Senior Safety Officers of Beams, Computing, and Technical Divisions

The BTeV Safety Officer resides in the Project Office and reports to the BTeV Project Manager. The Safety Officer's role is to develop plans and procedures for the safe execution of the project, provide advice on safety issues, review plans to make sure that ES&H issues are properly taken into account in their development and to monitor their execution for compliance, work as a liaison to other laboratory safety staff who provide oversight, and work with the BTeV experimental collaboration to develop procedures and training for safe execution of the Project. The BTeV Safety Officer is responsible for coordinating ES&H issues that cut across organization lines. The BTeV Safety Officer will work with the project personnel, external collaborators, and safety personnel in each Division and Section to insure that BTeV construction proceeds in a safe and environmentally sound manner and produces a safe and environmentally sound result.

The PPD Senior Safety Officer (PPDSSO) reports to the PPD Head and is responsible for ES&H issues in PPD. The PPDSSO has part of the ES&H oversight responsibility for the BTeV Project. The BTeV Safety Officer, assisted by the PPD Senior Safety Officer where required, coordinates any activities and facilitates the resolution of any issues that cut across various Divisions.

The AD Senior Safety Officer (ADSSO) reports to the AD Head and is responsible for ES&H issues related to the project that fall solely within AD. The ADSSO has part of the ES&H oversight responsibility for the BTeV Project. The BTeV Safety Officer and the ADSSO work to resolve any issues involving the AD that cut across divisional/sectional lines with the SSO's of all divisions involved in the issue.

The CD Senior Safety Officer (CDSSO) reports to the CD Head and is responsible for ES&H issues related to the project that fall solely within CD. The CDSSO has part of the ES&H oversight responsibility for the BTeV Project. The BTeV Safety Officer and the CDSSO work to resolve any issues that cut across divisional/sectional lines with the SSO's of all divisions involved in the issue.

The TD Senior Safety Officer (TDSSO) reports to the TD Head and is responsible for ES&H issues related to the project that fall solely within TD. The TDSSO has part of the ES&H oversight responsibility for the BTeV Project. The BTeV Safety Officer and the TDSSO work to resolve any issues that cut across divisional lines with the SSO's of all divisions involved in the issue.

There is an MOU in place between FESS and ESH in which the ESH Section provides construction safety oversight and support to FESS for ES&H issues related to the project that fall solely within FESS. The BTeV Safety Officer and ES&H and FESS personnel work to resolve any issues that cut across divisional lines with the SSO's of all divisions involved in the issue.

The Fermilab ES&H Section is ultimately responsible for oversight and advice on all ES&H aspects of the BTeV Project. The Senior Laboratory Safety Officer (SLSO) regularly reviews projects, operations, and experiments for applicability of the provisions of FESHM and makes corresponding recommendations to the Director concerning SAD/PSAD applicability. He has determined that a PSAD and SAD will be required for BTeV. The Directorate, advised by the ES&H Section, will determine the need for updates to the BTeV SAD. The results of updates will be incorporated into the final BTeV SAD. Additionally, in accordance with FESHM 2010, the project will coordinate the necessary Accelerator Readiness and Operational Readiness reviews. The SLSO makes additional determinations that are described in FESHM 2010.

3.13 BTeV Spokesperson

The BTeV Spokesperson provides the means of contact between the BTeV Collaboration and the Laboratory. He/she speaks for the Collaboration and represents the Collaboration in interactions with the Laboratory. The BTeV Spokesperson is responsible for all aspects of the BTeV Experiment, including the operation of the BTeV detector, the analysis of data and production of physics results. The Spokesperson is selected by the Collaboration. In doing so, the Collaboration consults with the Fermilab Director and he/she concurs in the selection. Scope changes that have the potential to change the physics reach or physics capability of the BTeV experiment, but which do not affect the mission need, will be initiated by the spokesperson and approved by the Fermilab Director. The Spokesperson, representing the Collaboration, and after detailed discussion with the BTeV PD, seeks approval for all scope changes with the potential to have a significant impact on the physics capability of the detector by making scientific proposals to the Fermilab Director. The Fermilab Director may seek the advice of the Physics Advisory Committee when considering these proposals. The Fermilab Director approves all such scope changes, those that increase the scope as well as those that reduce it. Depending on the cost of the proposed change, its impact on the BTeV Project schedule, or its interaction with other laboratory projects, programs and priorities, the Fermilab Director may need to seek approval of the change from the DOE.

3.14 BTeV Deputy Spokesperson

The BTeV Deputy spokesperson reports to the BTeV Spokesperson and represents the BTeV spokesperson in all BTeV Collaboration functions when the spokesperson is not available. The spokesperson may delegate some of his/her specific duties to the deputy. The Deputy Spokesperson is selected by the Collaboration. In doing so, the Collaboration consults with the Fermilab Director and he/she concurs in the selection.

3.15 BTeV Project Director

The BTeV Project Director (PD) provides oversight, coordination, management, and direction of the BTeV Project. The Project Director is responsible for developing and coordinating support for the project from various organizations including the BTeV Project, other units within the laboratory, and institutions in the Collaboration. This support includes engineering and design, procurement and fabrication, ES&H support, administration, financing, and scheduling. He/she represents the BTeV Project in interactions with the BTeV Collaboration, FNAL, DOE, NSF, U.S. Institutions participating in the BTeV Project and foreign institutions and funding agencies participating in the BTeV Project. The PD is appointed by the Director of Fermilab with the concurrence of the BTeV collaboration. He/she reports to the Fermilab Director (or his/her appointed representative). A non-Fermilab BTeV collaborator may be appointed as the Project Director after receiving a Guest Scientist appointment at the Laboratory. The Project Director reports to the Spokesperson on all technical and scientific issues of the BTeV detector.

Specific responsibilities of the PD include:

- a) Formulating, with the BTeV spokesperson and the BTeV Project Manager, the definition of the project and approving or, when additional approval is required, recommending any changes in the project scope, cost, or schedule.
- b) Approving the Technical Design Reports for each subsystem, with the concurrence of the BTeV spokespersons and the Fermilab Deputy Director.
- c) Concurring with the choice by the Fermilab Director of the Deputy PD and the Project Manager.
- d) Appointing, with the advice of the Project Manager and in consultation with the BTeV spokesperson, the Level 2 Managers who are responsible for coordination and management within each major subsystem.
- e) Preparing, with the Project Manager, annual funding requests to DOE and NSF for the anticipated BTeV Project activities. This takes the form of participating in the preparation of the annual Fermilab budget submission for DOE funding provided by Fermilab for the BTeV project.
- f) Upon the advice of the Project Manager and the Level 2 Managers, negotiating and implementing Memoranda of Understanding with all participating institutions for the total project scope of work and the annual Statements of Work associated with the annual work plan in support of the BTeV Project. MOUs form agreements between the BTeV Project and BTeV Collaborating Institutions,

specifying the deliverables to be provided, the schedule, and the resources available on an institution by institution basis.

- g) Approving changes to the scope, cost and schedule of the project above specified thresholds.
- h) Maintaining close coordination with the Fermilab Director or his/her delegate on the progress of the BTeV project, and reporting promptly any problems that might benefit from the joint efforts of the PD and the Fermilab Management.
- i) Interacting with Fermilab Management, and where appropriate with funding agency representatives, on issues affecting resource allocation and availability.
- j) Informing and advising DOE and NSF representatives at special meetings and reviews.
- k) Reviewing, approving, and transmitting the monthly report, prepared by the Project Manager, on activities, issues, performance and fiscal status of the Project
- l) Making periodic reports to the PMG and the various oversight boards, for example, the IFC, on the status and issues of the Project
- m) Making periodic reports to the BTeV collaboration and Executive Board to ensure that the BTeV collaboration is fully informed about all important issues
- n) Providing oversight of the project, including conducting internal reviews.
- o) Reporting to the Fermilab Deputy Director on all matters that have the potential to result in commitments of the Laboratory or the Universities Research Association.
- p) Exercising, as part of line management for the Project, the responsibility for completing the project safely and with respect for the environment.

3.16 BTeV Deputy Project Director

The BTeV Deputy Project Director reports to the BTeV Project Director and represents the BTeV Project in all functions when the Project Director is not available, including budget authority. The Project Director may delegate specific duties to the deputy, including budget authority. The Deputy PD is appointed by the Director of Fermilab and with the concurrence of the BTeV collaboration.

A non-Fermilab BTeV collaborator may be appointed as the Deputy Project Director after receiving a Guest Scientist appointment at the Laboratory.

3.17 BTeV Project Manager

The BTeV Project Manager (PM) has the responsibility and authority to manage the BTeV Project to the approved scope, cost, and schedule. The PM is appointed by the Director of Fermilab with the concurrence of the PD, and the BTeV collaboration. He/she reports to the PD. He/she assists the PD in representing the BTeV Project in interactions with the BTeV Collaboration, Fermilab, DOE, NSF, and U.S. Institutions participating in the BTeV Project and foreign institutions and funding agencies participating in the BTeV Project.

The responsibilities and authorities of the Project Manager, include:

- a) Managing the project to deliver the approved scope on schedule, within budget, safely, and with respect for the environment.
- b) Managing, coordinating, integrating, and planning the BTeV Project.
- c) Maintaining and updating the BTeV Project baseline cost and schedule plan;
- d) Proposing changes to the project scope, cost, or schedule above specified thresholds to the Project Director;
- e) Implementing and maintaining the BTeV Earned Value System;
- f) Acting as liaison with the Fermilab Management on Fermilab resources and infrastructure, performance milestones, departmental and divisional issues and self-assessments;
- g) With the Level 2 Managers, conducting Engineering Design Reviews and Production Readiness Reviews to ensure that project organization, integration, and interface issues are addressed.
- h) Preparing the monthly report and various annual and other reports and submitting them to the PD for approval and transmission
- i) Providing or arranging technical support for the Level 2 Managers so that they can accomplish their goals.
- j) Adjusting resources below specified thresholds among Level 2 Projects
- k) Ensuring the achievement of project milestones.
- l) Proposing and following up on corrective action when milestones are projected to be late
- m) Managing and approving major project procurements and supporting Level 2 Managers in preparing Request for Proposal/Quotations (RFP/RFQ's) and market surveys for large capital procurements
- n) Organizing, and chairing where necessary, production readiness reviews, BTeV Project Office reviews of L2 subsystems, drafting for approval reports on proceedings, and recommending and following up on proposed actions, if required.
- o) Providing overall schedule and technical integration
- p) Ensuring the preparation of Technical Design Reports for each subsystem.
- q) Appointing, with the advice of the relevant Level 2 managers and in consultation with the PD, Level 3 managers and proposing to the PD appointments and changes to the Level 2 managers
- r) Providing Quality Assurance, Risk Assessment/Management, Value Engineering, and Configuration Management for the BTeV Project.
- s) Managing and overseeing a BTeV Project Office within the Particle Physics Division.
- t) Ensuring that all elements of the project conform to applicable U.S. and relevant foreign Quality Assurance and ES&H requirements.
- u) Establishing standards and procedures by which the BTeV project is executed.
- v) Updating the Project Management Plan as necessary with the approval of the signatories to this document.
- w) Identifying the need for out-of-scope changes as they arise to the PD. When there is a need for a change having a significant impact on the physics capability of the

detector, the Project Director reports these to the Spokesperson. After consultation with the Technical Board, the PD identifies the need to the Fermilab Director through the PMG. Other changes follow the change control procedure described below.

- x) Assisting the Project Director in organizing presentations at reviews and status reports on the Project as needed to respond to the Fermilab Director and funding agencies.

The Project Manager has the responsibility of completing the Project on schedule, on budget, and within the agreed upon scope by managing the designated resources of the Laboratory and, in consultation with the Spokesperson, the designated resources of the Collaboration. He/she is responsible for monitoring expenditures of US and non-US funds. He/she tracks and reports deviations from baseline schedules and costs as specified in the Project Management Plan. The Project Manager reports to the PD on all matters related to managing the Project to the approved scope, cost, and schedule and on any changes that are proposed. He/she reports to the PD on all matters that have the potential to result in commitments of the Laboratory or the Universities Research Association.

3.18 Technical Coordinators

The Technical Coordinators, including the BTeV Project Mechanical Engineer, Electronics Engineer, and Software Engineer are appointed by the Project Manager with the concurrence of the PD and the BTeV Spokesperson. The Technical Coordinators report to the Project Manager and assist the Project Manager and the Project Director in the coordination, evaluation, and decision-making process for technical issues in the Project. They also assist the Project Manager in preparing the standards and procedures required to manage and execute the project.

3.19 BTeV Project Subproject Managers

The Level 2 managers are appointed by the Project Director, with the advice of the Project Manager and in consultation with the BTeV spokesperson. They report to the PM. The Level 3 Subproject Managers are appointed by the Project Manager with the concurrence of the PD. The Subproject Managers manage and direct their subprojects and report to the Project Manager. They are directly responsible for generating and maintaining the cost-estimate, schedule, and resource requirements for their subprojects. They are responsible for meeting the goals of their subproject within the accepted baseline cost and schedule. The Subproject Managers are in the line management for the project and are responsible for completing their subprojects safely and with respect for the environment.

3.20 BTeV Collaborator Responsibilities

The responsibilities of BTeV Collaborators are specified in comprehensive BTeV Memoranda of Understanding (MoU). A multi-year MoU details the work that the Collaborator has agreed to do for the Project, and includes a list of the personnel

involved, and significant milestones. These agreements are updated yearly through Statements of Work (SOW) that specify the funding and commitments for the next Fiscal Year. They are negotiated by the BTeV Project Director, in consultation with the Project Manager, and are approved by the Collaborator BTeV Contact Person, appropriate responsible parties for the collaborating institution, the BTeV Spokesperson, the heads of affected Divisions, and the Deputy Director. The Project Manager has responsibility for coordinating and managing all Collaboration-wide resources identified by these MoU's and SOW's.

3.21 Advisory Functions

3.21.1 BTeV Technical Board

The Project Director and Project Manager serve as co-chairs of the BTeV Technical Board that meets frequently to discuss technical and management issues in the Project and is advisory to the Project Director and Project Manager. The group is comprised of the BTeV Spokesperson, Project Director, Deputy Project Director, Project Manager, BTeV Safety Officer, Technical Coordinators, the WBS Level 2 Subproject Managers, additional personnel from the Project Office, and others as the need arises. It also has three at large members from the collaboration, usually drawn from universities or other national laboratories. It includes the BTeV offline computing project leader, the leader of the detector simulation project, and the leader of the BTeV event reconstruction project. The WBS Level 3 Subproject Managers often participate in these meetings. The Technical Board advises the Project Director and Project Manager on all aspects of the project including any changes to the cost, scope or schedule. It is the beginning of the change control process within BTeV and is the link to the BTeV collaboration for changes to the baseline through the participation of the BTeV Spokesperson. The meetings also provide a convenient mechanism for the dissemination of information.

3.21.2 BTeV Project Management Group

The Laboratory Deputy Director chairs a Project Management Group (PMG) that meets as required, but at least monthly, to monitor the progress of the project. The meetings are attended by those who have responsibility for the Project and by those who have authority to redirect resources within the Laboratory and the Collaboration. The group normally consists of the BTeV Spokesperson and Deputy, the BTeV Project Director and Deputy and Project Manager, the Heads of participating Divisions and Sections, ES&H Section Head or designee, the Laboratory Deputy Director, the Associate Director for Research, the Associate Director for Accelerators and other representatives of Fermilab and BTeV. The PMG also serves as the Change Control Board for the project.

3.21.3 BTeV Executive Committee

The BTeV Executive Committee consists of the leaders chosen by the BTeV collaboration, along with the BTeV spokesperson, to deal with collaboration and physics issues related to the experiment. It has strong university representation and has international balance. It advises the BTeV Spokesperson on all aspects of BTeV including collaboration issues relating to the BTeV Project.

3.21.4 BTeV International Finance Committee

The BTeV International Finance Committee consists of the BTeV Spokesperson, and a funding agency representative from each non-US country providing funding or in-kind contributions to BTeV. Since much of the U.S. contribution comes through Fermilab, the Fermilab Associate Director of Research is the U.S. funding agency representative on the committee and serves as chairperson. During the construction phase, the BTeV Project Director and Project Manager are also members. DOE and NSF representatives are invited to attend. This Committee oversees the use of financial contributions by these groups to the costs associated with the construction of the BTeV Project and operation the BTeV detector and experiment.

4 WORK BREAKDOWN STRUCTURE

All work required for completion of the Project is organized into a Work Breakdown Structure (WBS), a hierarchical ordering of tasks in outline-like form. The WBS constitutes a complete definition of the scope of the project and forms the basis for its planning, execution, and control. The foundation of the WBS for the technical components of the BTeV Project are the BTeV Technical Design Reports that thoroughly describe the design of the Detector, Interaction Region, and C0 Outfitting projects. The WBS consists of a resource-loaded cost and schedule (RLCS) with appropriately linked tasks. The schedule contains Materials and Services (M&S) costs, labor costs, and contingency on a task-by-task basis, as well as a series of project milestones that aid in the estimation of the project end date. The WBS structure to level 2 is shown in the organization and reporting chart above.

The major systems that comprise the Project are represented at WBS Level 2 are

WBS 1.0 The BTeV Detector:

- (1.1) Magnet, toroid and beam-pipes
- (1.2) Pixel Detector
- (1.3) Ring Imaging Cherenkov counter (RICH)
- (1.4) Electromagnetic calorimeter (EMCAL)
- (1.5) Muon Detector
- (1.6) Forward Straw Tracker based on straw detector technology that covers
- (1.7) Forward Silicon Microstrip Tracker
- (1.8) Trigger system
- (1.9) Data Acquisition (Event Readout and Control System)
- (1.10) Installation and Integration

WBS 2.0: The C0 Interaction Region

- (2.1) New Magnet Fabrication and Test
- (2.2) 2005 Shutdown (C0 Straight Section)
- (2.3) Power Supplies
- (2.4) Cryogenics
- (2.5) Controls
- (2.6) Instrumentation
- (2.7) ES Separators
- (2.8) 2008 Shutdown
- (2.9) 2006 Shutdown
- (2.10) 2007 Shutdown
- (2.11) 2009 Shutdown
- (2.12) Post-installation Acceptance Testing (Checkout)
- (2.13) Beam Physics

WBS 3.0 C0 Outfitting

- (3.1) C0 Outfitting Phase 1

- (3.2) C0 Outfitting Phase 2
- (3.3) C Sector High Voltage
- (3.4) Pre-procurement items

WBS 4.0 BTeV Project Management

The task-based WBS extends downward through many additional levels to facilitate cost, schedule and resource planning. The WBS structure through Level 2 for the Detector (WBS 1.0) and through Level 1 for C0 Interaction Region, C0 Outfitting and Project Office is described below.

WBS 1 BTeV Detector Project

This Level 1 summary element consists of all elements of the BTeV Detector Construction Project: Magnets, Toroids, and Beam-pipes; Tracking system – pixel detector, forward straw tracker, and forward silicon tracker; Particle Identification System –Ring Imaging Cherenkov Counter, Electromagnetic Calorimeter, and Muon Detector; Trigger and Data Acquisition System, and Installation and System Integration (I&I).

WBS 1.1 Magnet, Toroids, and Beam-pipes

This level 2 summary element covers the disassembly of the existing SM3 dipole magnet, its transportation to C0 and its reassembly with pole piece shims. It also includes assembling 4 toroid magnet sections in C0 using iron from the existing SM12 magnet. The last piece covers the installation of a thin 1” diameter beam-pipe from the pixel detector to the front of the RICH where it will be coupled to a recycled 2” diameter Be beam-pipe that was used by CDF in Run I.

WBS 1.2 Pixel Detector

This level 2 summary element covers the design, procurement, construction, and testing of a sophisticated, radiation-hard, silicon pixel vertex detector. This element includes the silicon pixel sensors, readout chip, readout electronics, mechanical supports, module production, cabling, vacuum system, assembly and installation, monitoring, software, and associated administration.

WBS 1.3 Ring Imaging Cherenkov Counter (RICH)

This level 2 summary element covers constructing two virtually independent systems sharing the same physical volume. The primary system consists of gas radiator ~3 m in length using C_4F_8O (or equivalent). The Cherenkov light is focused onto a photon detector using a thin spherical mirror. The photon detector is built from Multi-Anode-Photo-Multiplier tubes. The second system consists of a thin liquid C_5F_{12} radiator with the Cherenkov light going directly into a Photomultiplier tube array. The gas tight holding structure, electronics, cabling, monitoring and testing are also included.

- WBS 1.4 Electromagnetic Calorimeter (EMCAL)
 This level 2 summary element consists of a gas tight structure that holds ~10,000 PbWO₄ crystals, each connected to a Photo-multiplier tube and readout electronics. There is also an LED monitoring system. The cabling and testing of the system are also included.
- WBS 1.5 Muon Detector
 This level 2 summary element provides wire chamber based detectors arrayed among the toroid magnets that detect the presence of muons and provide an alternate trigger based on opposite signed dimuons. The gas system, holding scheme, electronics and testing are also included.
- WBS 1.6 Forward Straw Tracker
 This level 2 summary element provides for tracking charged particles in all but the inner regions of the spectrometer where the Forward Silicon System provides this function. WBS 1.6 includes wire chambers constructed with outer plastic elements surrounding each wire, hence “straws” the associated electronics, cabling and gas system. The system also provides some support for the inner Silicon Tracker. Testing is included.
- WBS 1.7 Forward Silicon Microstrip Tracker
 This level 2 summary element includes single sided silicon strip detectors the associated electronics, cabling and a cooling system. Testing is included.
- WBS 1.8 Trigger System
 This level 2 summary element includes specialized electronics and computing equipment that takes data from the pixel detector (primary) or the muon system (alternate) and makes a decision on whether or not to keep the raw data in a given interaction for further processing. It includes all cabling, software and testing.
- WBS 1.9 Data Acquisition System
 This level 2 summary element includes: hardware and software necessary to load data into the trigger and save it for further processing if required by the trigger; hardware and software to record the data to archival storage; and hardware and software to control and monitor the experiment. It includes cabling, computing equipment, software and testing.
- WBS 1.10 Integration and Installation
 This level 2 summary element contains planning, infrastructure, transportation to C0, and all things necessary to install the experiment that are not included elsewhere.

- WBS 2 C0 Interaction Region
This Level 1 summary element consists of all elements of the BTeV Project required to implement a high luminosity (low beta) interaction region in C0 to provide the luminosity required by BTeV. It also includes reconfiguration of C0 into a standard straight section to support BTeV parasitic commissioning, also known as Test Mode.
- WBS 3 C0 Outfitting
This Level 1 summary element consists of outfitting the C0 assembly hall with a three level counting room, and providing power, mechanical equipment and services. It also includes modifications to nearby service buildings and the addition of transformer pads and transformers.
- WBS 4 Project Management
This Level 1 summary element consists of reviews, reports, site visits, local supervision, running technical board meetings, standards preparation, tracking and analysis, schedule preparation tracking and analysis, change control. It also includes procurement of relevant software and computers and running the project office.

5 TECHNICAL, SCHEDULE, AND COST BASELINE

5.1 Technical Baseline and Technical Definition of Project Completion

The PEP contains the official scope of the Project, the technical baseline for which is further described in the BTeV Technical Design Report. The technical definition of “Completion” for each of the BTeV subprojects is shown in Appendix B Table 1. Project Completion is based upon full installation of detector components in the Collision Hall, complete installation of elements of the trigger and data acquisition system in the counting room, integration of all components, and checkout with source, pulsers and/or cosmic rays to verify the functionality of the BTeV detector components prior to operation with colliding beam; full installation and operation of all beam line elements at design power and successful operation of all devices, instrumentation, controls, and interlocks from the Accelerator Division Control System; and acceptance of all work performed for C0 Outfitting in accordance with the conditions set forth in the corresponding contracts.

The full detector will be completed towards the end of 2010. Operations with the full detector will begin in 2010/2011.

5.2 Project Schedule

A comprehensive schedule of work to design, construct, assemble, and commission the BTeV detector is maintained to facilitate management of the Project. It is comprised of detailed schedules for the development of each subsystem in the project and includes the resources (cost, manpower) required for each step. Based on these details, an overview of the project has been fashioned, complete with cost and manpower needs as a function of time and a series of milestones spread throughout the project. The WBS structure is defined through this schedule.

5.2.1 Schedule Methodology

The schedule is assembled using the computer program OpenPlan, created by the WELCOM Corporation. Subproject managers are responsible for the generation and maintenance of the schedules for their subsystems, in collaboration with the BTeV Project Office.

The schedule is built of tasks of various durations and milestones that are linked to describe the flow and interdependency of the work. The manpower required to complete each task is specified. Separate allocations are made for various types of technical

personnel – including mechanical and electrical engineers, designer/drafters and technicians, as well as physicists, both for Fermilab and non-Fermilab employers. Thus, profiles in time of various work groups are readily obtained to aid in the establishment of manpower requirements and the allocation of personnel as the Project evolves. By entering the average hourly labor cost for each type of manpower, labor cost profiles are extracted for each work group as well as the total labor cost for each subproject and for the entire Project.

The M&S funds needed to complete each task are determined and assigned directly to the tasks in the schedule. Cost plans for each subproject and for the full project are then derived. Using this information, a consistent and viable work plan is established by making appropriate adjustments to the schedule to yield an overall cost plan that matches the profile of funds available from the Laboratory and other sources, and a manpower plan that can be supported by the Laboratory. We note that for all M&S and labor estimates, a detailed Basis of Estimate (BoE) is provided that describes the foundation of and justification for the resources assigned to each task in the schedule. Cost Books have been prepared that provide the source documentation (quotes, invoices, etc.) and supplementary information used in preparing the BoE.

The scheduling program identifies the critical path (or paths) to completion of the Project. This feature calls attention to those tasks that have no ‘float’ or slack and that must therefore be carefully monitored to prevent delay in project completion. Knowledge of the critical path facilitates changes to optimize the work and to hasten completion.

5.2.2 Project Schedule Milestones

A baseline schedule that is consistent with the available funding and manpower resources has been assembled. The schedule is monitored by the Subproject Managers and the Project Manager. A hierarchical set of milestones, so called “tiered milestones,” have been established to track progress in the Project. At the lowest level (Tier 5), a comprehensive set of milestones is distributed throughout the duration of each subproject, with the Subproject Managers holding change control authority for the Tier 5 milestones. A subset of the Tier 5 milestones is selected to serve as Tier 4 milestones; the Project Manager monitors and holds change control authority for the Tier 4 milestones. The Tier 3 milestones are derived from a subset of Tier 4 milestones; the Deputy Director monitors and holds change control authority for the Tier 3 milestones. These “Director’s Milestones” are listed in Appendix B Table 5 below. The Level 2 milestones are derived from a subset of the Level 3 milestones; the DOE BTeV Project Director monitors and holds change control authority for Level 2 milestones. These are shown in Appendix B Table 4. The Level 1 milestones are derived from these. The Acquisition Executive monitors and holds change control authority for the Level 1 milestones as described in the PEP. The Level 1 milestones are listed in Appendix B Table 3 below. The Level 0 CD-4 milestone represents the Critical Decision dates for the project; the DOE Deputy Secretary monitors and holds change control authority for the Level 0 milestones as described in the PEP. The Level 0 milestones are listed in Appendix B Table 2 below.

5.3 Labor Requirements

The labor requirements are extracted from the resource-loaded schedule and are given in Appendix B Table 6 in units of person-years. The categories shown include all collaboration-wide physicist personnel (Physicist), technical personnel provided by collaborating institutions (Technical-University), and technical personnel provided by Fermilab (Technical-Fermilab). Note that physicist personnel, while fully integrated as a resource in the project schedule, is funded by non-Project sources and is not included in the Project cost.

5.4 Project Cost

The cost estimate for the Project covers all Materials & Services (M&S) and Salaries, Wages and Fringe Benefits (SWF) costs for the Project. It does not include the operating costs for detector components after they are installed in the Collision Hall or counting room and commissioned without beam.

5.4.1 Cost Estimate

The M&S costs and labor resources are estimated at the lowest (task) level in the Project Schedule. Contingency for labor and M&S is also estimated at the task level based on the guidelines described in sections 5.4.2 and 5.4.3. The Project Manager is able to review the costs at any level of detail by examining the roll ups of tasks within a given class. The cost estimates provided by the Subproject Managers are reviewed by the Project Manager in consultation with any technical experts that are deemed necessary to evaluate the cost estimates. The costs in the schedule are given in FY'05 dollars. Appropriate overhead and escalation is done external to OpenPlan, within the COBRA accounting program that is used to compute earned value. It is foreseen that all project tracking and accounting will be done within the COBRA structure for the duration of the Project.

5.4.2 M&S Contingency Estimation

There are two estimates of contingency made for the Project. One estimate is made by the WBS level 3 Subproject Managers at the lowest available level. It is based on detailed estimates of designs where available, and on the experience of the Subproject Managers and the engineering staff directly involved with the subsystem where a conceptual design exists. Guidelines for the estimation of the contingency have been provided, but may be overridden by the Subproject Managers in exceptional cases. Separate guidelines are provided for contingency on M&S and Labor. In addition, the Project Manager and Project Director construct a “top-down” estimate of the contingency based on past experience, DOE guidelines, and the fiscal history of similar completed projects. They make the ultimate determination of the M&S and labor contingency, taking their own estimate and that constructed by the lower level managers into consideration.

5.5 Cost Summary

The Total Estimated Cost (TEC) of the BTeV Project in AY dollars is \$193M, including \$50.6M in contingency. The Total Project Cost (TPC) for the BTeV Project in AY dollars is \$216.2M, including \$53.9M in contingency. An obligation profile showing the anticipated obligations by fiscal year is extracted from the schedule. Appendix B Table 7 shows the estimated cost with contingency broken out from the subsystem costs for the detector at WBS Level 2. It also shows the estimated cost for the CO IR subproject with contingency broken out, the estimated cost for the C0 Outfitting with contingency broken out, and finally the estimated cost for the Project Office with contingency broken out. Appendix B Table 8 shows the complete obligation profile, derived from the resource loaded cost and schedule, by fiscal year, and includes the R&D funding in FY04, FY05, and FY06, the cost of constructing operational spares for IR components. These latter two subprojects comprise the “Other Project Costs” that appear in Table 7.

6 RESOURCE PLAN

The planned funding profile for the BTeV Project can be found in Appendix B Table 9. It includes all sources of funding including those from DOE through Fermilab, US BTeV collaborators supported by DOE and NSF, Italian collaborators supported by INFN funding, and Russian and Chinese collaborators. All foreign sources are in-kind contributions applied toward projects from non-US collaborators. U.S. Universities support is from in-kind support of engineering and other technical personnel. To this point, three US universities, Syracuse, Wayne State and Vanderbilt, have agreed to provide forward funding. That is also taken in to account in the resource plan.

7 CHANGE CONTROL THRESHOLDS

Any change to the Project that does not alter the scope of the Project as defined above does not require a new proposal to be submitted to the Laboratory. Although the scope of the project is not affected, changes resulting in cost variations, changes of personnel assignments, or schedule impact are considered changes to the project plan that may require authorization to implement.

7.1 Change Control Procedures

Formal change control procedures will be used to track technical, schedule, and cost changes in the Project. Each such change requires the preparation of a Project Change Request (PCR) form. Each Project Change Request will be reviewed by the Project Manager. The BTeV PMG will function as a Level 3 Change Control Board for the project, and the Level 4 CCB will be formed from a subset of the BTeV Technical Board, chaired by the Project Manager, with additional personnel from the BTeV collaboration or Fermilab Divisions as needed. Subject to the change control levels described below, the Change Request may be forwarded to the BTeV PMG after approval by the Project Director, for approval by the Deputy Director. The BTeV Project Manager will maintain current records of all Change Requests and their disposition

7.2 Technical Change Control Levels

Minor technical changes consistent with the baseline technical design and affecting just one subproject must be approved by the Subproject Manager.

Technical changes that affect more than one subproject but that do not diminish performance must be approved by the Project Manager.

Major technical changes that are a significant departure from the baseline technical design must be approved by the Project Director who brings them to the PMG for final disposition. The Project Director acts as advocate for such changes before the PMG.

Technical changes that affect ES&H requirements, impact accelerator systems, or changes in scope that affect physics capabilities require a Change Request be submitted for consideration by the BTeV PMG and approved by the Deputy Director.

7.3 Schedule Change Control Levels

Changes that result in the delay of a Level 5 milestone by more than a month must be approved by the Subproject Manager.

Changes that result in the delay of a Level 4 milestone by more than a month must be approved by the Project Manager.

Changes that result in the delay of Level 3 Director's Milestones require a Change Request be submitted by the Project Director for consideration by the BTeV PMG and approved by the Deputy Director. The response to such a Change Request may be to initiate a plan to reallocate resources to recover the schedule, a plan to stage or descope the detector, or rescheduling of the milestone.

7.4 Cost Change Control Levels

Changes to the cost of a single item exceeding \$10K must be approved by the Subproject Manager.

Changes to the cost of a single item exceeding \$10K or a 10% increase in the Subsystem base cost during the previous 12 months must be approved by the Project Manager.

Changes in the cost of a single item exceeding \$100K or a \$250K increase in the project base cost during the previous 12 months require a Project Change Request be submitted for consideration by the BTeV Project Director to the BTeV PMG and approved by the Deputy Director.

7.5 Change Control Summary

Table 1 summarizes the Fermilab change control thresholds and responsibilities. Table 2 summarizes the DOE change control thresholds and responsibilities described in the PEP. The flowchart shown in Figure 2 describes the full BTeV Change Control process.

Figure 3 shows a sample Change Request form.

Table 1. Fermilab technical, schedule, and cost baseline control levels.

	Fermilab Deputy Director (Level 3)	BTeV Project Manager (Level 4)	Subproject Manager (Level 5)
Technical	Major technical changes that are significant departures from the technical baseline. Changes that affect ES&H requirements or impact accelerator systems. Out-of-scope changes to upgrade physics capabilities.	Related technical changes to multiple subprojects that do not diminish performance .	Minor technical changes to a single subproject that do not diminish performance.
Schedule	Any change that results in the delay of a Level 3 Director's milestone.	Any change that results in the delay of a Level 4 milestone by more than one month.	Any change that results in the delay of a Level 5 milestone by more than one month
Cost	Increase in the cost of a single item by more than \$100K. Increase in the Project base cost exceeding \$250K during the previous 12 months.	Increase in the cost of a single item by more than \$10K. Increase in a subsystem base cost exceeding 10% during the previous 12 months.	Increase in the cost of a single item by less than \$10K.

Table 2:. DOE technical, schedule, and cost baseline control levels from the PEP.

	Secretarial Acquisition Executive (Level 0)	Acquisition Executive (Level 1)	DOE BTeV Project Director (Level 2)
Technical	Any change in scope and/or performance that affects mission need requirements.	Addition or deletion of major subsystem.	
Schedule	6 month or greater increase (cumulative) in the original project completion date.	Any change to level 1 milestones.	Any change to level 2 milestones (see PMP).
Cost	Increase in excess of \$25M or 25% (cumulative) of the original cost baseline.	Any increase in Total Project Cost and/or increase in Total Estimated Cost.	Any use of contingency that would take the contingency as percentage of TPC ETC below 28%.

In-Scope, Non-Directed Project Change Request (PCR) Flow Process

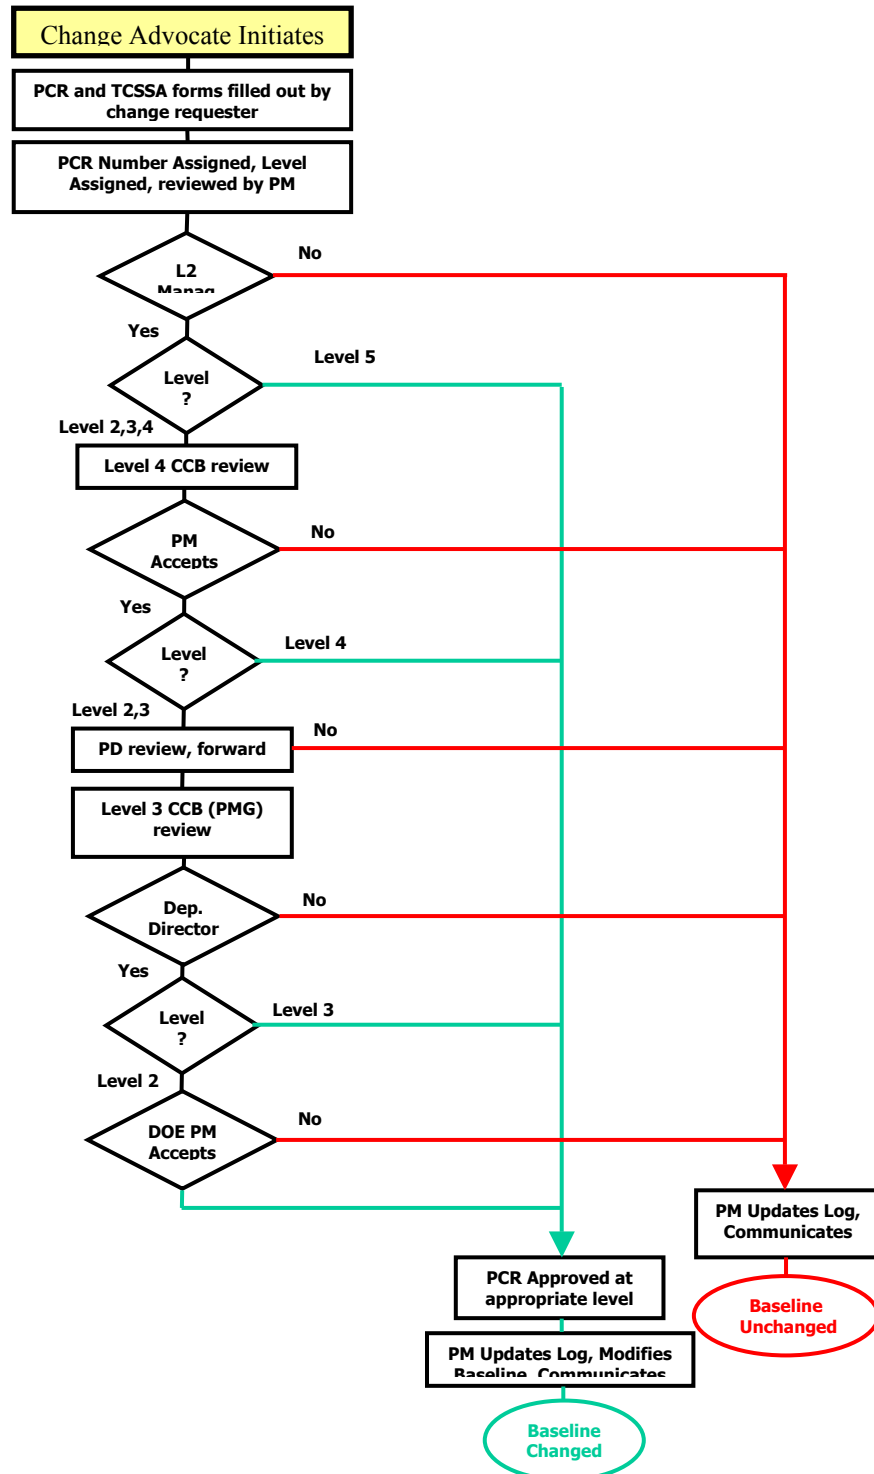


Figure 2: Change Control Flow Chart for in-scope, non-directed change.

BTeV Project Change Request (PCR) Form	
PCR No: <small>(Assigned by PM)</small> PCR Title: Originator: Change Type: <input type="checkbox"/> Technical <input type="checkbox"/> Schedule <input type="checkbox"/> Cost	Date: Co-Sponsor:
WBS No:	
Change Description:	
<hr/> <div style="display: flex; justify-content: space-between;"> <div> DOE Directed Change: <input type="checkbox"/> YES Urgent: <input type="checkbox"/> YES DOE Approval <input type="checkbox"/> Required If urgent, please explain </div> <div> <input type="checkbox"/> NO <input type="checkbox"/> NO <input type="checkbox"/> Not Required </div> </div> <hr/>	
Level of Change <input type="checkbox"/> 1 <input type="checkbox"/> 2 <input type="checkbox"/> 3 <input type="checkbox"/> 4 <input type="checkbox"/> 5	
CCB Review done: <input type="checkbox"/> Level 3 <input type="checkbox"/> Level 4	
Disposition: L3 Manager approved: <input type="checkbox"/> Yes <input type="checkbox"/> No Signature/date:	L2 Manager approved: <input type="checkbox"/> Yes <input type="checkbox"/> No Signature/date:
PM approved: <input type="checkbox"/> Yes <input type="checkbox"/> No Signature/date:	Other approval: <input type="checkbox"/> Yes <input type="checkbox"/> No Signature/date:
Project Director: <input type="checkbox"/> Approved Signature/Date: <input type="checkbox"/> Disapproved	
FNAL Director: <input type="checkbox"/> Approved Signature/Date: <input type="checkbox"/> Disapproved	
DOE BTeV Project Director: <input type="checkbox"/> Approved Signature/Date: <input type="checkbox"/> Disapproved	
PCR Disposition: <input type="checkbox"/> Accepted <input type="checkbox"/> Not Accepted	
Implementation Date:	

Figure 3. Sample Change Request form.

8 RISK MANAGEMENT

The BTeV Risk Management Plan (RMP) provides a structured and integrated process for identifying, evaluating, tracking, abating, and managing project risks in terms of three risk categories: cost, schedule and technical performance. The following is a summary of key aspects of the RMP. A general discussion of risk may be found in Section 7 of the Acquisition Strategy for the BTeV Project .

Any project faces both threats and opportunities and must strive to exploit the opportunities while ensuring that the threats do not derail the project. Numerous informal and formal approaches are used for identifying threats and opportunities, assessing their likelihood, prioritizing them for possible mitigation or exploitation, and devising strategies to do so. The key to successful risk management is alertness to potential risks and a deliberate approach to accepting, preventing, mitigating, or avoiding them. The BTeV project becomes aware of potential risks in many ways, notably during work planning, meetings, reviews, and via lessons learned from others. Routine meetings, such as weekly Technical Board meetings, routine WBS Level 2 system meetings, and monthly progress meetings, provide important forums for identifying, discussing, and resolving key risk areas and developing and adopting mitigation plans. Risk has been managed during the planning and design phase by implementing appropriate actions, such as ensuring adequate contingency and schedule float, pursuing multiple parallel approaches, and/or developing backup options. Detector construction projects are well within the experience and expertise of the BTeV collaboration. Every effort has been made to specify these projects in a manner that reduces the risk to an acceptably low level.

The technical risks facing the BTeV Project are no greater than those facing other HEP projects, and as in them, risks that are identified will be managed as early as possible to assure that they do not derail the timely completion of the project or stress its budget in unexpected ways. The initial risk assessment indicates the project will have low cost, schedule, and technical risk exposure, with the exception of the Pixel Detector and EMCAL, which were assessed to have a moderate risk level. Another source of moderate risk affects schedule, and it is due to potential delays in the appropriation and release of project funding.

8.1 Risk Management Responsibilities

The BTeV Project Director has delegated the responsibility for overall project risk management to the BTeV Project Manager. The Project Director is responsible for approving the risk management approach and providing oversight for the BTeV risk identification and mitigation process. The BTeV Project Manager develops the Risk Management Plan (RMP), which includes a Risk Management Board (RMB) that he/she chairs. The composition and purpose of the RMB are described in the RMP. The BTeV Quality Assurance Program Coordinator functions as a Risk Management Coordinator to help the Project Manager carry out his/her responsibilities in this area.

Because contingency is one of the major resources available to deal with problems arising during project execution, the management of cost, schedule and technical risks and the management of contingency are closely linked. Proactive risk identification and mitigation can therefore reduce pressure on contingency, by reducing the probability of unpleasant surprises that could require contingency to resolve.

8.2 Types of Risk

8.2.1 Technical Risk

Preparation of clear and concise specifications, judicious determination of subcontractor responsibility and approval of proposed lower tier sub-subcontractors, and implementation of QA provisions will minimize technical risk. The BTeV Project has been designed to further minimize technical risk by exploiting previous experience to the greatest extent possible, and minimizing exposure to single vendor failures.

Making deliberately conservative design choices, where possible, and carrying out extensive detector R&D where new technologies are involved has minimized technical risk throughout the BTeV Detector Project. Use of single sided sensors for the forward microstrip tracker, extensive R&D on the silicon pixel detector and the RICH readout, use of a switch based on commercial off-the-shelf components in the data acquisition system, reduction in component variety, and common integrated circuit technologies wherever possible will reduce risk. In all cases, the expertise of personnel involved in the design and implementation of previous versions of BTeV systems have been exploited to the fullest possible extent. Moreover, institutional commitments have been carefully crafted within the subprojects in order to help ensure timely and successful completion of the Project.

8.2.2 Cost Risk

Use of fixed-price subcontracts and competition will be maximized to reduce cost risk.

8.2.3 Schedule Risk

As outlined in Section 7.3 of the ASP, schedule risk will be minimized via:

- Aggressive R&D, including bench testing and beam testing
- Realistic planning,
- Verification of subcontractor's credit and capacity during evaluation,
- Close surveillance of subcontractor performance,
- Advance expediting, and
- Incremental awards to multiple subcontractors when necessary to assure total quantity or required delivery.

Incentive subcontracts, such as fixed-price with incentive, will be considered when a reasonably firm basis for pricing does not exist or the nature of the requirement is such that the subcontractor's assumption of a degree of cost risk will provide a positive profit incentive for effective cost and/or schedule control and performance.

In addition, the Project will be tracked monthly, with schedule changes carefully monitored and approved through a change control process overseen by a combination of the Project Manager, the Laboratory Directorate, and DOE (see section 8 of this document).

8.3 Risk Analysis

BTeV project risks are analyzed by considering their likelihood or probability of occurring together with the consequence to the project's technical performance, cost, and/or schedule baselines. Probability is assessed qualitatively as very low (0.01- 0.09), low (0.10 - 0.24), moderate (0.25 – 0.49), high (0.50 – 0.60), very high² (0.61- 0.99).

Consequence relates to the potential impact of the risk event on cost, schedule, and/or the technical baselines. Each risk event will be evaluated on these three aspects using the criteria and thresholds given in the BTeV Risk Management Plan (RMP). The highest (worst) consequence determines the overall consequence rating for the risk event. Consequences are characterized as Low, Moderate, or High.

Based on the combination of the probability and consequence ratings, risks are classified as high, moderate or low in accordance with the categorization provided in the RMP.

8.4 Risk Management Tools and Process

The Risk Management Process consists of a five step process: 1) identifying potential project risk, 2) analyzing project risk, 3) planning risk abatement strategies 4) executing risk abatement strategies, and 5) monitoring the results of and revising risk abatement strategies. These are described in detail in the BTeV RMP.

Risk management is a line activity in BTeV and, as such, will be a normal part of many activities and meetings. The BTeV Project Management meetings will take up risk issues from time to time. The BTeV Technical Board, which meets weekly, will also regularly include reports from Level 2 managers that will address risk-related issues. Level 2

² Subprojects used very high (0.61 - 0.80) and extremely high (0.81 – 0.99). Since no risk event was assigned "extremely high", the two categories were combined into a "very high" category for the project level analysis to reduce the size of the risk classification table.

subproject managers will be responsible for maintaining their project risk data in the same OpenPlan Database that they use for scheduling. A “watchlist” will be generated from this database to assist the Project Manager in carrying out his activities. Detailed descriptions of the processes and tools used by BTeV are given in the RMP.

9 PROJECT CONTROLS SYSTEM

9.1 Introduction

This chapter summarizes the BTeV Project Management System Description (PMSD) document that describes the management systems that the Project will use to monitor the cost and schedule performance and the technical accomplishments of the Project. The significant interfaces that exist among the various management systems are noted in the individual narrative descriptions below. Although these systems are described separately they are mutually supportive and will be employed in an integrated manner in order to achieve the project objectives. As conditions change during the evolution of the project, the management systems will be modified appropriately so as to remain responsive to the needs for project control and reporting. Consequently, while the policy and objectives of each management system will remain fixed, the methods, techniques, and procedures that will be employed by the Project may change as conditions dictate, over the life of the project.

The Work Authorization and Contingency Management System and the Project Control System described in this chapter define the management and control procedures required by the Laboratory.

9.2 Guidelines and Policies

The Contingency Management System and the Project Control System employed by the Project will be consistent with the Fermilab Director's Policy No. 12, dated January 1, 1999.

The following policies are applicable for the BTeV Detector Project:

- All Project work is organized in accordance with the WBS.
- Formal (and informal) reviews by experts are used to establish baseline specifications and designs.
- Established cost, schedule, and technical baselines are used for measuring project performance. Technical baselines are maintained in the Technical Design Reports describing the current design implementation for each system included in the scope of the Project. These will be updated as required to reflect approved changes and will be controlled documents once an initial technical baseline is approved.
- Changes to the approved cost, schedule and technical baselines proceed via a Change Request process described below.
- A project management system that features performance measurement based on cost accounting and scheduling is used to control the project and to provide forecast and feedback information to management. In particular, Earned Value will be calculated via the cost accounting tool COBRA, which uses as input the OpenPlan BTeV Project schedule.

- The decision-making apparatus includes regular meetings between the Project Manager and the Subproject Managers. These meetings help to identify and resolve interface issues within the project.
- Quality assurance, safety analysis and review, and environmental assessment are integral parts of the Work Authorization and Project Control.

9.3 Work Authorization and Contingency Management

Funds will be made available by the Director to the Project on an annual basis following the receipt of the Initial Financial Plan from DOE. These funds will correspond to a financial plan and a funding profile to project completion as determined by the Director. The funding profile will include contingency in each year of the project.

Work packages will be established by the Fermilab Budget Office following the WBS structure. The accumulation of M&S costs in these accounts will be initiated through purchase requisitions originating with the engineering and scientific staff assigned to the various subsystems. Signature authority levels will be provided to the Fermilab Business Services Section by the Project Director to assure that only authorized work is initiated.

At any time, the project contingency is the difference between the project Total Estimated Cost (TEC) and the Estimate at Completion (EAC). The Project Director will hold the contingency and allocate it subject to the Project Control System described below.

The principles of contingency management that the Project will follow are as follows:

- The cost estimate for each subsystem will include contingency funds based on an assessment by the preparer, in conjunction with the PM, of uncertainties and risks associated with the budgeted cost;
- The actual use of contingency will be reflected in a new EAC to be updated periodically;
- The Deputy Director will approve all Change Requests that will require utilization of contingency, subject to the thresholds described in section 7.4 above;
- All changes will be tracked with approved Change Requests and a record of all Change Requests will be maintained by the Project;
- Each fiscal year, the Project Director will assign the contingency available in that year within the following guidelines:
 - The Project Manager may adjust the estimated cost of any WBS level 2 subproject by as much as \$100K, as long as the Project TEC is not exceeded. If the change exceeds \$100K, the Change Request must be approved by the Deputy Director;

- The use of contingency above the amount budgeted for the year requires that a Change Request be approved by the Deputy.
- All changes from baseline cost shall be traceable.

9.4 Baseline Development

Baseline development includes management actions necessary to define project scope and responsibilities, establish baselines, and plan the project. Each subproject prepares a formal cost estimate and schedule. The subprojects all have defined Work Breakdown Structures (WBS) which are detailed subsets of the WBS, below level 2. In addition, technical specifications for each subproject are contained in the Technical Design Reports. The BTeV Detector Technical Design Report includes detailed technical descriptions of all detector systems, the trigger and data acquisition systems, integration and installation, and pre-beam commissioning. The C0 Interaction Region Technical Design Report describes all aspects of the design and implementation of the high luminosity IR for C0. The C0 Outfitting Technical Design Report describes the design and implementation of work to provide the facilities required in C0 to support the BTeV experiment and the IR.

9.5 Project Performance Measurement

Project Performance includes management actions after work commences that are necessary to monitor project status, report and analyze performance and available resources, and manage risk. Project performance aspects of the Project Control System consist of the following:

9.5.1 Funds Management

The detailed obligation plan for each WBS item is derived from the baseline schedule for the project that is funded at a rate consistent with the profile of funds from the Laboratory and other sources. This top-down obligation plan is adjusted by Project Management as appropriate to reflect changes in the Laboratory funding profile.

9.5.2 Accounting

A record of all M&S obligations associated with individual WBS elements is maintained in the Project financial system for tracking purposes. Each obligation is identified with the corresponding cost account, thereby enabling comparison of obligations with the Cost Estimate at that level. Monthly tracking reports are produced that show all purchasing activity at the cost account level in each subproject. For each item, as well as roll-ups to higher levels, the cost estimate, current-year allocation, year-to-date and project-to-date obligations and balances are displayed.

All BTeV Project M&S transactions are also associated with Fermilab work packages, generally at WBS level 5 or below. The Fermilab financial system is used to track and account for all obligations and subsequent costs at level 4 and above. Monthly accounting reports depict obligation and cost details and summaries for all work packages or WBS categories at and above level 4. The cost of labor in each WBS level 2 category in the BTeV Project is captured by reporting the fraction of effort of each individual involved in the work and transferring the salary cost to the corresponding budget code.

The financial system accommodates the allocation of direct costs collected from a single point to multiple control accounts. This is accomplished through split coding. The split codes are tracked through the work packages in question and are reflected in the monthly reports.

9.5.3 Performance Measurement and Analysis

The principle functions of performance measurement and analysis are to identify, quantify, analyze and rectify significant deviation from the plan as early as possible. Earned-value reporting will be accomplished through the use of the COBRA software package.

9.5.4 Schedule Variance

At the end of each month, the detailed schedule for each subproject is examined for variances from the baseline schedule. This is accomplished by updating the 'actual' schedule on the basis of work performed in the period, and comparing the actual schedule to the baseline schedule. An extensive set of milestones for each subproject is also monitored. This is performed by the WBS Level 2 and Level 3 Managers, and submitted to the Project Management for examination and review.

Changes that have a significant impact on the project, either by delaying completion or by affecting the cost or manpower plan of the project, are identified for further analysis. A plan to rectify the problem is developed that may include:

- alteration of the schedule to optimize the work and reduce the delay,
- allocation of additional resources (funds or manpower) to shorten the time required to perform given tasks.

Any change that would alter the schedule, cost or personnel resources of work to be performed is subject to the controls described below.

9.5.5 Cost Variance

In approving a purchase requisition, the WBS level 2 managers will compare the proposed obligation with the balances remaining for that item and its parents at higher levels. If the obligation does not exceed the estimated cost, the manager may approve the requisition directly. However, if the obligation would require use of contingency on that item or at a higher level, the manager must formulate a plan to fund the item and attach the details to the requisition for approval by the Project Manager. In this fashion, use of contingency is approved prior to incurring the obligation. Cost variances that exceed the established thresholds are formally reported as provided in section 7.

Each month, obligation performance is determined by comparing obligations to date with budgeted or allocated costs to date as indicated by the obligation-loaded schedule.

9.5.6 Resource Variance

On a monthly basis, the available funds and manpower resources are compared with those required in the schedule to identify shortfalls that could lead to schedule and/or cost variances. Any such variances will be brought to the attention of the BTeV PMG.

9.6 Change Management

Change management includes the actions necessary to ensure adequate control of project baselines, including the performance measurement baseline. Details regarding change control at DOE Levels 0 and 1 are contained in Section 7 of the PEP. Change Management aspects of the Project Control System consists of the following:

9.6.1 Out-of-Scope Changes

An out-of-scope change is a proposed change to the scope of the Laboratory-approved Project that would alter the physics capabilities of the detector in a major way or introduce a new detector system. The 'scope' of the project includes the design, construction and installation of the collection of systems or improvements to systems that have been granted Stage I approval by the Director. The scope of the project is defined by the proposal document that includes content equivalent to a Technical Design Report. Each individual system or an improvement to a system has an impact on the physics capability of the Project as a whole. This physics capability is also defined in the proposal. The scope of the project as an aggregate determines the physics capabilities of the upgraded detector.

Any out-of-scope change must be initiated by a formal proposal by the Spokespersons to the Director for consideration. In response to such a proposal, the Director may seek the advice of the Fermilab Physics Advisory Committee, the BTeV PMG and/or a Director's Review. Such a proposal may be granted Stage I approval, deferred for further clarification of the physics potential, technique, cost and/or schedule, or it may be rejected. Depending on the cost of the proposed change, its impact on the BTeV Project schedule, or its interaction with other laboratory projects, programs and priorities, the Fermilab Director may need to seek approval of the change from the DOE.

9.6.2 In-Scope Changes

Any change to the Project that does not alter the scope of the Project as defined above does not require a new proposal to be submitted to the Laboratory. Although the scope of the project is not affected, changes resulting in cost variations, changes of personnel assignments or schedule impact are considered in-scope changes. The change management for in-scope changes is fully described above on the mechanism for baseline change control.

9.7 Reporting and Review

9.7.1 Monthly Progress Reports

The Project provides reports on a regular basis to Fermilab and DOE management. The objective of the reporting is to provide for the collection and integration of essential technical, cost, schedule and performance data into reports to aid in the monitoring and management of the Project.

All WBS Level 2 Managers submit monthly written reports to the Project Manager detailing specific progress on the pertinent subsystems. These reports summarize the activities of the previous month, describe activities planned for the upcoming month, and

include comments and concerns. They are collected and summarized in a corresponding monthly report submitted to the Heads of the Particle Physics Division, the Computing Division, the Technical Division, the Accelerator Division, FESS and the Directorate that outlines progress, problems, and budget and schedule status, including comparisons of projected status versus actual status. The Directorate submits these reports to the DOE.

9.7.2 Technical Design Reports

A comprehensive Technical Design Report has been written that includes detailed technical descriptions of all BTeV Detector Project subsystems: detector components, trigger and data acquisition systems, integration and installation and pre-beam commissioning. This report provides the basis for the technical baseline of the BTeV Detector Project. The C0 Interaction Region Technical Design Report describes all aspects of the design and implementation of the high luminosity IR for C0. The C0 Outfitting Technical Design Report describes the design and implementation of work to provide the facilities required in C0 to support the BTeV experiment and the IR. The linkages and dependencies of these three projects are not especially complex and are captured in the Resource Loaded Cost and Schedule.

9.7.3 Meetings and Reviews

Various meetings between the Directorate, Project Management, Subproject Managers and the Collaboration will be held at appropriate intervals to ensure management of the overall project.

9.7.3.1 BTeV Project Management Group (PMG)

Meetings will be convened by the Deputy Director to monitor the progress of the project, as described in Section 3.20.2.

9.7.3.2 BTeV Technical Board

Frequent meetings between the Project Management and the Subproject Managers, as described in Section 3.20.1, will take place throughout the life of the project. Full discussion of all issues related to the status of the Project – technical, schedule, cost, personnel issues and needs – are covered here on a regular basis.

9.7.3.3 General Project Meetings

Eight to twelve general project meetings will be held each year that will provide the opportunity for project participants at every level to present status reports, discuss current issues and disseminate news and information. Whenever possible, these meetings will be synchronized with BTeV Collaboration meetings, held approximately monthly. These meetings are of general interest to anyone involved in the Project and serve to integrate diverse activities and provide an opportunity for physicists to criticize work in areas other than their own in this large project.

9.7.3.4 Subproject Meetings

Meetings shall be called by Subproject Managers, typically at a bi-weekly interval, to discuss status, progress, and issues directly related to the pertinent subproject, as well as its coupling to other parts of the Project. Possible departures from schedule and cost, and their mitigation, are discussed in these meetings prior to a more general presentation to and discussion with the BTeV Technical Board.

10 ACQUISITION STRATEGY

The acquisition strategy is detailed in the Acquisition Strategy for the BTeV Project. In the following sections we summarize this document.

10.1 Construction and Fabrication

Fabrication of components and subsystems will be done in-house using Fermilab facilities, by outside vendors working under subcontract to the Laboratory or BTeV collaborating institutions, and by BTeV collaborators at their home institutions. The responsibilities of each participating institution are further described in Memoranda of Understanding between the Project and the participating institution.

10.2 Procurement Plan

The components of the BTeV Project will be acquired in a manner consistent with DOE and general Fermilab guidelines. Whenever possible, fixed-price competitive procurement practices will be followed. Purchase requisitions will be processed by the Fermilab procurements group after appropriate approval or by delegation to procurements groups of participating institutions.

10.3 Inspection and Acceptance

The Project Manager will be responsible for assuring that the appropriate procedures are in place at the subproject level to ensure that components and assemblies are inspected sufficiently to assure satisfaction of technical specifications. The subproject manager is responsible for devising appropriate inspections. Acceptance of components and systems will be done by those individuals directly responsible for them. When appropriate, inspection visits will be made to vendor shops, collaborating institutions and industrial firms fabricating or preparing components for the project.

10.4 System Testing and Check out

Once components are assembled and integrated into a subsystem, 'system tests' will be performed. These tests will involve the activation, debugging and tune-up of the full subsystem. Though such tests pertain to the system under study alone, they may require other subsystems to be operational to enable the tests. Examples of system tests include tests of the pixel detector readout system, response of the electromagnetic calorimeter to its calibration light source, and operation of the pixel and muon triggers on simulated data.

Check out consists of the process of integrating working subsystems into an operational experiment, and is the final stage of preparation for actual data taking. At this stage interactions and potential conflicts between distinct detector, trigger and readout systems are confronted for the first time. The check out process will evolve gradually, as subsystems are assembled and system tests performed. Lastly, full operation of the detector in the Collision Hall will begin.

11 TECHNICAL CONSIDERATIONS

Technical considerations are presented and examined in detail as part of the Technical Design Reports for BTeV Detector, C0 IR, and C0 Outfitting. A brief summary of the research and development considerations is presented here.

BTeV began by defining a high level set of requirements needed to achieve its mission goals. R&D was undertaken on detector technologies that were plausible candidates to meet the requirements. After the R&D was completed, the best technology in each area one was chosen for the baseline. Considerations that entered into the choice included, but were not limited to, technical performance, construction cost, impact on the schedule, degree of risk, ability to successfully integrate and interoperate with the rest of the detector, robustness of operation, lifetime cost including operation, maintenance and removal, and the capability and experience of the project team with the technology. In some cases, when two choices appeared to be very close, we chose one as the baseline but continued R&D on the other as an “option.” This creates competition that should result in lower costs.

The R&D included simulation, prototyping, bench-testing, and testing with particle beams. Development work on BTeV was, in many cases, similar to work going on elsewhere in High Energy Physics. An effort was made to benefit from the work of other groups and in some cases direct collaborations were undertaken. Wherever possible, BTeV used commercial solutions rather than in-house designed approaches. As a result, there is a complete and stable baseline, with only a few options, and many of the subsystems are well along into their design phase. R&D will continue in FY05 and will finish with a small effort in FY06. In all cases, this R&D is directed towards optimization or to choosing between two alternatives each known to meet the requirements.

Research and development is performed on detector components to ensure that the chosen technology will meet the physics and engineering requirements of the detector. Designs are documented in design reports and drawings are checked by peers, senior engineers, and/or managers. Design reviews are performed. Design reports, specifications, drawings and other documentation will be delivered to FNAL to ensure that detector components can be supported and maintained.

12 QUALITY ASSURANCE PROGRAM

Quality Assurance is an integral part of the design, fabrication and construction of the BTeV Project. Special attention is paid to items that are most critical to the schedule and performance requirements of the Project. All work performed at Fermilab will draw on the guidelines and criteria set out in the Fermilab Director’s Policy Manual, section 10. These include:

- management criteria related to organizational structure, responsibilities, planning, scheduling, and cost control;
- training and qualifications of personnel;
- quality improvement;
- documentation and records;
- work processes;
- engineering and design;
- procurement;
- inspection and acceptance testing;
- assessment

Quality Assurance and Quality Control (QA/QC) systems are designed, as part of the Quality Management Program, to ensure that the components of the detector meet the design specifications and operate within the parameters mandated by the requirements of the High Energy Physics Program. The Quality Management Program can be found in Appendix B of this document. The QA/QC elements currently in place for the BTeV Project draw heavily on the experience gained from past detector construction projects. Senior management recognizes prompt identification and documentation of deficiencies, coupled with the identification and correction of the root causes, are key aspects of any effective QA/QC Program. The Project Manager endorses and promotes an environment in which all personnel are expected to identify nonconforming items or activities and potential areas for improvement.

Detector components are fabricated specifically for BTeV by either commercial vendors, other Department of Energy Laboratories, member universities within the BTeV Collaboration, Fermilab owned facilities, or some combination of the above. The items manufactured may be individual components, detector sub-assemblies, or a complete piece of upgraded equipment being installed as part of the Project. One example of a complete assembly would be the RICH detector, supplied by Syracuse University. It is the responsibility of the Project Manager and/or Project Leaders to have adequate verification methods in place to assure that only properly trained, qualified, and certified personnel are involved in the design, manufacture, and installation of detector components.

All components must be fabricated to pre-determined design specifications that will allow them to operate properly when integrated into the total system. Agreements will be in place with each vendor that explicitly state the operating parameters of the piece or pieces they construct. These agreements will also assign the responsibilities for testing and verification of the final product. Procured items must meet established requirements and perform as specified. In some cases, random testing of a certain percentage of components will be performed and documented by an independent organization. In the event that non-conforming items are discovered, they will be documented and controlled to preclude inappropriate use until compliance with the applicable technical requirements is demonstrated. Vendor qualifications are reviewed as part of the bid process and are

taken into consideration prior to bids being awarded. Vendor site visits may be conducted periodically throughout the duration of the fabrication contracts to ensure quality requirements are understood and being adhered to properly. Every electronic system should have as an essential part of its deliverable a fully documented testing and trouble shooting procedure.

Within Fermilab facilities, a Traveler will accompany each component through the assembly process. These information packets are used to identify, report, correct, and trend non-conformance situations adverse to quality detector performance. The Travelers will contain whatever historical information accompanies the equipment, list the specified operating parameters, and provide a place for testing results to be entered. The test results and certifications will then be compared to the required specifications and a determination will be made as to the final use or disposition of the item. It should be noted that testing and verification for performance within proper operating parameters will occur multiple times throughout the construction process as was the case during past detector construction projects. This multi-tiered testing approach will ensure that improperly installed, faulty, or failed components are detected at the earliest possible opportunity and allow immediate remedial action to be taken without jeopardizing or negatively impacting detector operation.

13 VALUE ENGINEERING

Value Engineering (VE) is a process by which costs can be reduced through an analysis of a products function, without sacrificing its performance and quality. The focus on a reduced cost, enhanced value relationship, determined through a functional analysis is integral to the design process for large scientific projects. The process itself is done in a different fashion than is generally employed in an industrial or construction setting. The BTeV Project and Fermilab are committed to VE principles in the design and construction of the experiment and associated infrastructure. VE is accomplished in the BTeV Project through an extensive design review process which each subproject and component is subject to before beginning construction. This peer review process takes place in external reviews conducted by the Fermilab and the Department of Energy, and in internal reviews to determine baseline costs, technical adequacy, and production readiness. As discussed in Section 12, systems are designed, as part of the Quality Management Program, to ensure that the components of the detector meet the design specifications and operate within the parameters mandated by the requirements of the High Energy Physics Program. Value Engineering in the BTeV Project is part of that process, which is further discussed in Appendix C.

14 CONFIGURATION MANAGEMENT

Configuration management refers to the techniques used to version and tag the components of the project in order to identify and track the configuration at all times throughout its construction and its operational lifetime. The BTeV Project uses several

tools to achieve this objective. These include a document control system that supports versioning and document signoff to “approve” a version; drawing management systems; a software control, versioning and release system based on a software repository; and a “parameter control system”, based on an XML-based “parameter book.”

15 INTEGRATED SAFETY MANAGEMENT

This section describes the policies for ensuring that Environmental, Safety and Health (ES&H) considerations are adequately addressed within the BTeV Project activities. The information below provides an overview of key issues. ES&H is a line management responsibility and will be implemented down through the subsystem organizations. Fermilab has many procedures and practices for ensuring that its work is accomplished in compliance with its ES&H program, which has been developed based on the Work Smart set of standards contractually agreed to by DOE. BTeV will adhere to these procedures and practices. Where BTeV-specific issues need to be addressed, specific information will be incorporated into BTeV ES&H plans (such as Hazard Analysis plans and Operational Readiness Plans).

The Project Manager, with the advice and assistance of the Safety Officer, will determine when internal safety reviews are required, will arrange for those reviews, and will follow up on any recommendations and findings. In doing so, the Project Manager will follow wherever possible existing procedures and practices and take advantage of standing committees that in many cases already exist to carry out ES&H reviews. The Project Office Engineering support is also available to help with the technical aspects of safety issues. The Project Manager may also request resources from the PPD Safety group and the Fermilab ES&H Section.

Safety issues will be addressed regularly at the BTeV Technical Board meetings. The Safety Officer will be a member of the Technical Board. The Safety Officer will address issues that arise that pertain to the BTeV Collaboration either by means of written reports, procedures and memoranda. At the invitation of the BTeV Spokesperson, The Safety Officer will talk about safety issues at BTeV Collaboration meetings.

The BTeV Project Manager, with the assistance of the Safety Officer, is responsible for providing, as required, specific requirements and procedures, as well as hazard assessments, and other documents to comply with DOE and FNAL requirements. BTeV ES&H documents are defined in the BTeV Operations Guidelines Manual.

Those who are on the BTeV project at the FNAL site will be provided with the training and information necessary to reduce the risks associated with their work and to ensure their safety. Briefings and presentations will be made to all managers and supervisors to communicate ES&H policies, documentation and information associated with assuring safety of BTeV activities. Job-specific training will be provided on issues including electrical safety, cryogenic safety, radiation safety, and chemical safety, as well as issues related to detector transportation, installation, and testing activities. Proficiency testing is

performed to gauge comprehension.

All visitors to BTeV will be informed of FNAL ES&H rules and procedures applicable to their visit. In general, visitors will not be allowed to work in areas without the advance permission of the BTeV Project Manager (PM) or his designee. All visitors to BTeV must be accompanied by a Host who is familiar with FNAL and BTeV ES&H rules and procedures. Hosts are responsible for the safety of the visitors they accompany.

APPENDIX A: List of Referenced Documents

BTeV Detector Technical Design Report

C0 Interaction Region Technical Design Report

C0 Outfitting Advanced Conceptual Design

BTeV Memoranda of Understanding and Work plans for each sub-project

Justification of Mission Need

Fermilab Project Control Systems Guidelines, May 1, 1994.

Acquisition Strategy [for the] BTeV Project at Fermi National Accelerator Laboratory

DOE Project Execution Plan for the BTeV Project at Fermi National Accelerator Laboratory

Fermilab Environment, Safety, & Health Manual (FESHM)

BTeV Project Management System Description (PMSD)

BTeV Risk Management Plan (RMP)

A Guide to the Project Management Body of Knowledge, ©2000 Project Management Institute

APPENDIX B: Cost and Schedule Tables

This Appendix contains tables with information on the BTeV costs, schedule, milestones, labor requirements and available funding. This information will be change when a formal BTeV baseline is accepted and, thereafter, when the baseline changes as a result of the change control process.

A brief definition of completion for each subproject is shown here:

B 1: Technical definition of Project Completion for WBS 1.0, 2.0, and 3.0

Subsystem	Technical Definition of Completion
1.1 Magnets, Toroids, Beam pipes	Operation of all magnets in C0 IR at design current and verification of design field, beam pipe installed and vacuum pumped down to acceptable level.
1.2 Pixel Detector	Complete system test with operation of pixel stations installed inside the pixel vacuum tank.
1.3 RICH	System test with 95% all sensors operational successful. Observation of Rings from Cosmic rays or beam spray
1.4 EMCAL	System test with 95% of all crystals successful. Observation of signals from pulsers on each channel.
1.5 Muon Detector	System test with all planes at voltage and successfully read out. Observation of signals from cosmic rays.
1.6 Forward Straw Tracker	System test with stations at voltage and successfully read out. Observation of signals from cosmic rays.
1.7 Forward Microstrip Tracker	System test with all planes at depletion voltage and noise observed on all channels.
1.8 Trigger	Complete system installed and interfaced to pixel and muon systems and meeting requirements based on checkout with simulated data
1.9 Data Acquisition	Readout of all detectors and observation of either noise signals, pulser signals, or cosmic rays depending on the detector
1.10 Integration	Complete installation of detector, with all components having all services required to operate, and all detectors interfaced to data acquisition and slow controls
2.0 C0 Interaction Region	All magnet and ES separator components surveyed on the beamline and operating at full power. All instrumentation and control hardware and software operational/
3.0 C0 Outfitting	All building and electrical work complete as specified and final acceptance issued for all construction contracts

Critical decisions and the DOE completion milestone is shown here.

B 2: Critical Decisions and DOE Level 0 (BTeV Tier 0) milestones for the BTeV Project.

	Description	Baseline Date
	CD-0: Approve Mission Need	2 nd Quarter FY04
	CD-1: Approve Alternative Selection and Cost Range	4 th Quarter FY04
	CD-2: Approve Performance Baseline	2 nd Quarter FY05
	CD-3a: Approve Limited Construction	2 nd Quarter FY05
	CD-3b: Approve Start of Construction	4 th Quarter FY05
0.1	CD-4: Approve Start of Operations or Project Closeout	3 rd Quarter FY11

Doe Level 1(BTeV Tier1) milestones are monitored by the BTeV Acquisition Executive or designee. The baseline date is the milestone date in the Project Baseline.

B 3: DOE Level 1 (BTeV Tier 1) Milestones for the BTeV Project

No.	WBS	Milestone	Baseline Date
1.1	2.0	Start quadrupole fabrication	Oct. '06
1.2	3.0	Beneficial occupancy of lower level and upper staging area	Aug. '06
1.3	1.1	Vertex magnet installed in C0 and powered	Feb '07
1.4	1.2	Purchase Order awarded: Production pixel hybridization	Jul. '06
1.5	1.4	20% of PWO Crystals accepted	Mar. '08
1.6	1.2	Pixel System assembled and tested at SiDet, ready to ship to C0	May. '09
1.7	2.0	IR Components (that will be installed in tunnel) installed and powered	Nov. '09
1.8	1.4	EMCAL Crystal procurement completed	Mar. '10
1.9	1.0,1.10	Detector complete and ready for commissioning with beam	Apr. '11

DOE Level 2 (BTeV Tier 2) Milestones are monitored by the DOE BTeV Project Director, who resides in the Fermilab Site Office (FSO). These are shown in Table B4 below. Level 1 milestones may also appear as Level 2 milestones.

B 4: DOE Level 2 (BTeV Tier 2) Milestones for the BTeV Project.

No.	WBS	Milestone	Baseline Date
2.1	1.1	Vertex Magnet installed in C0 and powered	Mar. '07
2.2	1.2	Purchase order awarded: Production pixel readout chip	Feb. '06
2.3	1.2	Purchase order awarded: Pixel sensors	Nov. '05
2.4	1.2	Purchase Order awarded: Production pixel hybridization	Jul. '06
2.5	1.2	Pixel System Tested /ready to install in C0	May, '09
2.6	1.3	Rich Tank ready to Install in C0	Aug. '08
2.7	1.3	Purchase order awarded: Production MAPMTs	Oct. '05
2.8	1.4	Purchase order awarded: Production QIE chips	Dec. '05
2.9	1.4	20% of PWO Crystals accepted	Mar. '08
2.10	1.4	75% of PWO Crystals accepted	Jul. '09
2.11	1.4	EMCAL Support structure assembled	Jun. '08
2.12	1.5	Beginning of octant production	Jun. '07
2.13	1.6	Purchase order awarded: Production ASDQ chips	Oct. '05
2.14	1.6	Station 1 ready for installation in C0	Oct. 09
2.15	1.7	Readout IC approved for production	Jan. '07
2.16	1.7	First FSIL station ready to be installed in C0	Apr. '09
2.17	1.8	Trigger pilot system ready for testing	Sep. '07
2.18	1.8	First production release of Level 2/3 Trigger software	Mar. '09
2.19	1.9	Data Combiner Board pre-production units tested and approved	Sep. '06
2.20	1.9	Multinode release of Data Acquisition RCS package	Mar. '08
2.21	2.0	Start quadrupole fabrication	Oct. '06
2.22	2.0	IR Components done and ready for installation	May '09
2.23	3.0	Start C0 Outfitting Construction	Jun. '05
2.24	3.0	Beneficial occupancy of lower level and upper staging area	Aug. '06
2.25	3.0	C0 Outfitting construction complete	May '08
2.26	2.0	IR components installed and under power	Oct. '09
2.27	1.0, 1.10	Detector complete and ready for commissioning with beam	Feb. '10

DOE Level 3 (BTeV Tier3) milestones are monitored by the Fermilab Director in conjunction with the BTeV Project Manager. These are shown in Table B5 below. Level 1 and Level 2 milestones may also appear as Level 3 milestones.

B 5: DOE Level 3(BTeV Tier 3) milestones, a.k.a “Fermilab Director’s milestones, for the BTeV Project

No	WBS	Milestone	Baseline Date
3.1	1.1	Magnets, Toroids, Beam pipes	
3.2		Vertex Magnet parts complete	Jun. ‘06
3.3		Vertex magnet ready for installation	Mar. ‘07
3.4		1 st Toroid parts acquisition completed	May ‘07
3.5		South Toroid ready for installation	Mar. ‘07
3.6		North Toroid ready for installation	Mar. ‘08
3.7		Beam pipe rework begins	Nov. ‘07
3.8		RICH beam pipe ready for installation	Aug. ‘09
3.9		Forward tracking Beam pipe ready for installation	Sep. ‘09
3.10	1.2	Pixel Detector	
3.11		Purchase order awarded: Pixel sensors	Nov. ‘05
3.12		Purchase order awarded: Pixel readout chip	Jan. ‘06
3.13		Purchase order awarded: Pixel detector hybridization	Jul. ‘06
3.14		10% system assembled and ready for C0	Dec. ‘06
3.15		Vacuum system designed and approved for construction	Aug. 07
3.16		Start final detector assembly	Oct. 07
3.17		Production pixel module completed	Apr. ‘08
3.18		Pixel system tested, ready for install at C0	May ‘09
3.19	1.3	RICH	
3.20		Start MAPMT Production	Jan. 06
3.21		All MAPMTs delivered	May ‘08
3.22		MAPMT Hybrid (VA-BTeV) Production started	Feb. ‘06
3.23		MAPMT Hybrid Production completed	Jan. 07
3.24		Mirror Segment Construction done	Apr. ‘07
3.25		Gas radiator RICH detector completed	Aug. ‘09
3.26		Liquid Radiator PMTs Procurement complete	Jan ‘09
3.27		Liquid radiator assembly complete	May ‘09
3.28	1.4	EMCAL	
3.29		Purchase order awarded: First EMCAL Crystals	Jul. ‘05
3.30		EMCAL Crystal Procurement completed	Mar. ‘10

3.27		ADC card checkout completed	Nov. '08
3.28		QIE Packaged parts tested	Mar. '06
3.29		PMT Procurement completed	Feb. '09
3.30		Assembly of EMCAL complete	Sep. '10
	1.5	Muon detector	
3.31		End of Octant Pre-production	May '07
3.32		15% of Production Planks completed	Jan. '08
3.33		Start Octant Production	Jun. '07
3.34		Purchase order awarded: long term production ASDQ ICs	Mar. '06
3.35		20% of Production front end boards completed	Aug. '06
3.36		First Muon Station ready for installation	Jun. '08
3.37		Muon Detector Completed	Jun. '10
	1.6	Forward Straw Tracker	
3.38		Purchase order awarded: Production ASDQ chips	Oct. '05
3.39		ASDQ chip procurement completed	Aug. '06
3.40		Preparation site functional	Mar. '06
3.41		Production/assembly sites functional	Jan. '07
3.42		Station 1 ready for installation in C0	Oct. '09
3.43		Station 7 ready for installation in C0	Aug. '09
	1.7	Forward Silicon Tracker	
3.44		Sensor accepted for full production	Jun '07
3.45		Production sensors received and tested	Mar. '08
3.46		Readout IC approved for production	Jan. '07
3.48		Production ICs received, tested and thinned	Jun. '07
3.49		Hybrids approved for production	May '07
3.50		Hybrids complete and tested	Aug. '08
3.51		Station support procurement complete	Oct. '08
3.52		Ladder production 100% Complete	Mar. '09
3.53		First FSIL station ready to be installed in C0	Apr. '09
3.54		Last FSIL station ready to be installed in C0	May '09
	1.8	Trigger	
3.55		Start L1 2-highway pixel processor and segment tracker production	Sep. '07
3.56		End L1 2-highway pixel processor and segment tracker production	Feb. '09
3.57		Start L1 2-highway farm production	Sep. '07
3.58		End L1 2-highway farm production	Dec. '08
3.59		Start L2/3 farm worker node procurement	Jan. '08

3.60		Start Level 3 software development	Oct. '05
3.61		First production release of Level 2/3 software	Mar. '09
3.62		Complete trigger system and integration with DAQ	Feb. 10
	1.9	Data Acquisition System	
3.63		DCB pre-production units tested and approved	Sep. '06
3.64		Production DCB delivered and tested	Feb. '09
3.65		Production Level 1 Buffers delivered and tested	Feb.'09
3.66		Single node release of RCS package	Oct. '07
3.67		Data Acquisition software complete	May '09
3.68		Calibration and Trigger database complete	Nov. '08
	1.10	Integration, Installation, and testing	
3.69		Purchase order awarded: Production of HV Power supplies	Oct. '07
3.70		High Voltage Power Supply Delivery Complete	Jan. '09
3.71		Vertex Magnet, South Toroid installed	Mar. '07
3.72		North Toroid Installed	Mar. 08
3.73		RICH Tank Installed	May '09
3.74		EMCAL Support structure (partially loaded) installed	Aug. '09
3.75		Trigger, Data Acquisition System installed	Sep. '10
3.76		All other detector subsystems installed	Sep. '10
	2.0	C0 Interaction Region	
3.77		Collar Lamination Steel Received	Mar. '06
3.78		Begin quadrupole production	Oct. '06
3.79		Issue RFP for HTS leads	May '05
3.80		Issue RFP for corrector magnets	Mar. '05
3.81		Start fabrication of spool assembly	Dec. '06
3.82		Quadrupole fabrication and test completed	Sep. '09
3.83		Spool assembly fabrication/test completed	Jun. '09
	3.0	C0 Outfitting	
3.84		Start C0 Outfitting Construction	Jun. '05
3.85		Occupancy C0 :Lower level and upper staging area	Jul. '06
3.86		Collision Hall completed	Feb. '08
3.87		Assembly, service building construction completed	May '08
	4.0	Project Office	
3.88		Staffing complete	Apr. '05
3.89		Effort reporting in place	Dec. '04
3.90		Begin monthly reports	Dec. '04

Table B6 contains the staffing plan for the BTeV Project including physicist and technical labor.

B 6: Staffing plan for physicist and technical manpower. Units are person-years

	FY 2005	FY 2006	FY 2007	FY 2008	FY 2009	FY 2010	Total
Physicist	52	93	114	97	40	22	418
Technical- University	13	39	39	28	9	3	131
Technical- Fermilab	50	87	103	96	43	22	401
BTeV Total	115	219	256	221	92	47	950

Table B7 shows the base cost in AY M\$, the contingency as a percentage of the base, and the total cost for each subproject for the entire duration of the BTeV Project.

Table B7: Base Cost and Contingency by Subproject (AY M\$)

WBS	Description	Base M\$	Contingency M\$	%	Total M\$
1.1	Magnets, Toroids, Beam-pipes	2.280	0.544	23.9%	2.825
1.2	Pixel Detector	13.918	5.889	42.3%	19.807
1.3	RICH	12.417	3.969	32.0%	16.385
1.4	EMCAL	16.273	6.779	41.7%	23.051
1.5	Muon	4.577	1.722	37.6%	6.299
1.6	Forward Straw Tracker	10.038	2.602	25.9%	12.641
1.7	Forward Silicon Tracker	7.455	2.644	35.5%	10.099
1.8	Trigger	10.936	4.946	45.2%	15.882
1.9	Event Readout and Control	13.829	4.763	34.4%	18.592
1.10	Installation and Integration	10.610	5.247	49.5%	15.857
1	Cost BTeV Detector	102.334	39.105	38.2%	141.439
2	Cost C0 IR	27.308	8.699	31.9%	36.007
3	Cost C0 Outfitting	6.031	1.288	21.4%	7.319
4	Cost BTeV Project Office	6.789	1.635	24.1%	8.423

Table B8 shows the Obligation profile by Fiscal Year (in AY M\$) by Level 1 subproject. In addition, the BTeV Detector Subproject is broken down to WBS Level 2. Total Estimated Cost (TEC) is \$193M AY. Total Project Cost is \$216M AY.

B 8: Obligation profile for entire BTeV project by Level 1 subproject.

BTeV Project Estimated Obligation Profile (AYM\$)								
WBS#, Subproject	FY04	FY05	FY06	FY07	FY08	FY09	FY10	Total
1.1 Analysis Magnet, Toroids		0.06	1.32	0.39	0.32	0.18	0.00	2.28
1.2 Pixel Detector		0.58	5.96	4.00	2.95	0.43	0.00	13.92
1.3 RICH Detector		0.13	3.64	4.83	3.12	0.71	0.00	12.44
1.4 EM Calorimeter		0.29	1.23	4.41	7.52	2.54	0.00	15.99
1.5 Muon Detector		0.30	1.91	1.45	0.91	0.00	0.00	4.58
1.6 Forward Straw Tracker		0.70	4.24	2.54	2.31	0.12	0.04	9.95
1.7 Forward Silicon Strips		0.66	2.25	2.47	2.00	0.08	0.00	7.46
1.8 Trigger System		0.12	1.28	3.11	2.52	3.89	0.02	10.94
1.9 DAQ System		0.13	2.68	3.08	4.86	2.97	0.10	13.83
1.10 Integration and Installation		0.05	0.73	1.54	3.17	2.25	2.63	10.37
2.0 C0 Interaction Region		2.66	5.49	8.84	7.14	2.98	0.20	27.31
3.0 C0 Outfitting		1.00	2.75	2.28	0.00	0.00	0.00	6.03
4.0 Project Management		0.50	1.14	1.22	1.23	1.40	0.75	6.24
Equipment Base Estimate		7.18	34.63	40.17	38.06	17.56	3.75	141.34
Equipment Est. Contingency		2.06	11.98	11.52	12.90	13.18	0.00	51.64
Total Estimated Cost (TEC)		9.24	46.61	51.69	50.96	30.74	3.75	192.98
IR Spares		0.45	1.32	1.40	1.88	0.67	0.00	5.72
IR Spares Contingency		0.17	0.50	0.40	0.56	0.27	0.00	1.89
R&D FY05-FY06	6.00	6.51	1.47	0.01	0.00	0.00	0.00	13.99
R&D Contingency		1.14	0.33	0.00	0.00	0.00	0.00	1.47
Total Project Cost (TPC)	6	17.51	50.22	53.49	53.40	31.68	3.75	216.05

Table B9 shows the Funding Profile for BTeV based on Fermilab budget guidance and guidance on support from INFN. Three BTeV Universities have agreed to forward funding arrangements amounting to \$9.5M and those are included as well. Total Anticipated Budget Authority (all sources) is \$216 M AY.

B 9: Planned funding profile for the BTeV Project.

BTeV Project Funding Profile (AYM\$)								
	FY04	FY05	FY06	FY07	FY08	FY09	FY10	Total
DOE OPC	6.0	6.3	2.2	3.05	3.12	2.4	0	23.1
MIE DOE		6.75	39	48.15	48.58	42.5	0	184.98
Total DOE	6.0	13.05	41.2	51.2	51.7	44.9	0	208.1
Forward Funding		3.05	6.45	0	0	-9.5	0	0
INFN		1.42	2.57	2.29	1.71	0.03	0.00	8.02
Total Anticipated BA FY04-FY10	6.00	17.52	50.22	53.49	53.41	35.43	0.00	216.07

APPENDIX C: Quality Management Program

1. PROGRAM**1.1 BTeV Project Mission**

The mission of the Fermilab BTeV Project is to support the Fermilab High Energy Physics (HEP) research program by constructing a new detector for use at the C0 interaction region. The Directorate approves HEP experiments and allocates funds to provide the facilities, personnel, and equipment required to achieve successful completion of this mission. The BTeV Project Office is responsible for ensuring the quality of the support mechanisms, all FNAL fabricated items, and non-FNAL supplied items that may have either an operational impact or an Environmental, Safety, and Health (ES&H) impact. This responsibility includes assuring proper integration of the new detector into the existing building infrastructure as well as establishing and enforcing Department of Energy (DOE) requirements. The Project Manager must ensure that the Project structure and organization are appropriate for effectively carrying out this mission.

1.2 Organization

The BTeV Project is composed of the Project Management Office and three main working groups. These three working groups are organized according to the Work Breakdown Structure (WBS) assigned to the Project and are listed in the main body of the BTeV Project Management Plan (PMP) and an organization chart is maintained by the Project Manager. General descriptions of the primary functions for the groups are also found in the Project Management Plan. Level 2 Managers set QA goals and objectives pertaining to their work environments and periodically assess progress toward them.

1.3 Roles, Responsibilities, and Authorities (RRA's) for Quality

RRA's for Quality flow down through the Project as outlined in the Fermilab Quality Assurance Policy, Section 10 of the *Director's Policy Manual*. The Project Manager assigns the QA/QC function to the appropriate manager for the BTeV Project. Stop Work Authority related to quality of work has been delegated to all management and supervisory personnel within the Project. They are authorized and expected to halt unsatisfactory work being performed by any of the individuals or organizations reporting to them. The Division Head, Project Director, and Project Manager may specify other stop work authority outside of the normal management chain at their discretion.

2. PERSONNEL TRAINING AND QUALIFICATION**2.1 Scope**

The Project supports Fermilab efforts with respect to personnel training and qualification, and believes that maintaining a trained and qualified work force is instrumental in

ensuring the quality of products and services provided by the Project. This section describes the responsibilities and requirements necessary to provide the Project with qualified personnel who possess the appropriate level of skill, experience, and academic qualifications to support the achievement of the Project mission and performance objectives.

The Project Manager requires that all Project personnel be trained and have the appropriate experience to ensure that they are capable of performing their assigned work in a safe and efficient manner. This training must reflect the fact that the Project's scope of work involves the collaborative effort of personnel who have widely divergent levels of education, skills, and experience.

2.2 Education and Qualifications

Line management will ensure that assigned personnel have the appropriate level of qualifications. Qualifications may be job related experience or skills; technical and/or professional society certifications; formal education; or any combination thereof.

The education that is required for obtaining a university/college degree (or other professional certification) constitutes qualification for working within the discipline in which the degree was granted. Equivalent work experience and technical activity in a related discipline may also constitute acceptable qualifications.

2.3 Specific Job Related Training

When it is determined that an employee needs specific job related training in order to effectively and efficiently carry out duties that are assigned, training will be made available to the employee. In-house training will be provided to ensure that an appropriate level of skills, knowledge, expertise, and experience are available to accomplish stated mission and objectives. Training may come from several sources such as mentoring, or be provided by physicists, engineers, supervisors, lead personnel, consulting firms, QA personnel, ES&H personnel, and/or other sources.

In order to ensure that training skills are maintained at an appropriate level, an Individual Training Needs Assessment (ITNA) is required for each employee on an annual basis or whenever a change in job assignment and/or job hazards occurs. The annual training needs assessment shall be performed and reviewed with each employee in conjunction with the Fermilab Employee Performance Review process. This shall include a review of employee training needs with respect to the work the employee is expected to perform or hazards to which the employee would be exposed during the normal performance of the assigned job.

Managers are chosen for their technical and communication skills. The Project does not specify any further training or education for these personnel beyond what they initially bring to their positions. However, the Project Manager may also require further technical training for key personnel.

Supervisors within the support groups outside of the Project are chosen by their Department Heads. Supervisory positions include Deputy Department Heads and Group Leaders. These personnel are selected primarily for their technical abilities. If deemed useful by the Department Head, an individual supervisor may be required to attend the Supervisory Development course taught by Laboratory Services Section (LSS). The Department Head may also require additional training or education, oriented toward development of technical and/or supervisory skills, but there are no generally applicable requirements mandated by the Project.

3. QUALITY IMPROVEMENT

3.1 Scope

Achieving quality is a line responsibility. The Project encourages personnel to eliminate problems and improve performance. Managers are encouraged to use statistical methods or other management tools to help make the decisions necessary to improve quality for their operations. These methods may serve as a basis for trending, for continuous quality improvement from lessons learned, or to help foster a positive attitude toward quality initiatives. Managers are also encouraged to document non-conformances and identify, analyze, resolve, and follow up on recurring problems.

The Project has a strong commitment to continuous quality improvement in all areas and activities for which it is responsible. All levels of personnel are encouraged to report performance problems and maintain a "no fault" attitude toward individuals identifying concerns. Stop Work Authority related to quality of work is described above in Section 1.3, Roles, Responsibilities, and Authorities for QA. The objective is to identify a problem, to promptly report it to the appropriate level of management for corrective action, and for management to take the necessary corrective action commensurate with the programmatic significance or importance of the problem.

3.2 Identification/Reporting of Concerns and Non-conformances by Employees

A series of regular meetings have been established to allow employees to report and discuss performance problems. Project management has regularly scheduled weekly meetings to assess the progress of Project initiatives. Level 2 and 3 Managers present status reports at these meetings and free and open discussion of concerns is encouraged. Lessons learned are thus disseminated and are also utilized for additional feedback concerning quality improvements. Each Project group has its own methods for evaluating problems and performance. These include regular meetings and discussion by appropriate supervisory and technical personnel.

3.3 Documentation and Reporting

Quality non-conformances identified during operations, inspections, and design reviews shall be documented as appropriate. For problems with Fermilab-procured items and services, the Business Services Section (BSS) Procurement Department should be provided with details regarding non-conformances as specified below in Section 7.4, Verification of Acceptable Quality.

Quality non-conformances for products and services procured outside of the Fermilab system are to be reported to the Project Manager by the appropriate Level 2 Manager. Procured items that do not meet Project specifications must not be used. It is the responsibility of the organization that received the items to properly segregate the material and decide on its final disposition.

4. DOCUMENTS AND RECORDS

4.1 Document Control

The Project determines which records require document control as part of the Configuration Management Program. These records are controlled for reasons of personnel safety as well as for legal and/or historical purposes.

4.2 Records Retention and Disposition

Records produced within the Project must be retained. A disposition schedule must be created and maintained in accordance with Fermilab guidance. Examples are the Technical Design Report (TDRs), Project procedures, Basis of Estimate (BoE) documents, survey results, non-conformance reports, design drawings, QA Travellers, etc. Records that are not forwarded to Fermilab as part of component shipments are not subject to Fermilab requirements.

5. WORK PROCESSES

5.1 Work Process Control

The Project Manager requires that each Level 2 and 3 Manager develop means for analyzing work processes to determine if the work is sufficiently complex or hazardous to be performed to written procedures. The responsibility for determining which work processes require procedures rests with the Department Head or Group Leader responsible for the activity. Guidelines for performing these determinations can be found in the Particle Physics Division Operating Manual as part of PPD_OPER_004, Integrated Safety Management.

5.2 Maintaining an Effective and Efficient Work Force

The Project Manager requires that each Level 2 and 3 Manager strive to maintain an effective and efficient work force. The Project attempts to appropriately utilize personnel skills in the assignment of work responsibilities. Ensuring that the Project successfully

meets its objectives is accomplished by assigning personnel to particular tasks who have the appropriate skills, experience, academic qualification, or professional certification to complete the work. The Project relies on line management to monitor activities to successful completion and to take necessary steps to incorporate added expertise and effort when indicated. More detailed information is provided in Section 2.0, Personnel Training and Qualification, above.

5.3 Measuring and Test Equipment (MTE) Calibration

The necessity for calibration and control is dependent upon the application and criticality of the equipment. The Project Manager requires that each Level 2 and 3 Manager analyze their work process measuring and test equipment to determine the appropriate calibration requirements and develop an effective program for the necessary calibration activities.

6. DESIGN

6.1 Scope

Equipment designed by Project personnel follows federal codes; the *Fermilab Environment, Safety and Health Manual*; Laboratory standards; and accepted industry standards. Relevant personnel are required to incorporate sound engineering and scientific principles and appropriate technical standards into designs to ensure that they will perform as intended.

6.2 Design Interface

In some cases, the Project relies on organizations outside of Fermilab to generate complete design packages. Examples include the RICH, Forward Silicon Tracking, and the Muon Detector systems. Each collaborating institution agrees to the scope of work they will undertake for the Project by means of a Memorandum of Understanding (MOU) and specific Statement of Work (SOW). These documents are generated and kept on file by the Project Office and reviewed at appropriate times in order to keep them current.

6.3 Project Reviews and Operational Clearances

Hazard assessments are performed by the Project at the initial design stages. The information from these hazard assessments is used to determine what reviews are necessary for the experimental apparatus. These are also used to develop the Operational Readiness Clearance (ORC) checklists for the Project. The Project must have an ORC completed, signed, and accepted prior to start-up.

The Project Manager may commission ad hoc technical review panels from within the Laboratory or the BTeV Collaboration to review experimental apparatus when the need arises. The Project Manager also has the option to request assistance from the Laboratory Safety Committee for equipment reviews involving resources outside of the

Project. Examples of this would be cryogenic systems, wire targets, flammable gas systems, mechanical apparatus, etc.

7. PROCUREMENT

7.1 Scope

This section describes the Project's program to ensure that procurement practices are in accordance with established Fermilab policies. Collaborating universities are only bound to Fermilab's procurement requirements in cases where Fermilab actually participates in the procurement process.

7.2 Equipment and Services Procurement

The BTeV Project procurement guidelines follow the *Fermilab Procurement Policy and Procedures Manual*. This manual, produced and maintained by the Business Services Section, includes instructions for the preparation of purchase requisitions and dictates responsibility for review and approval.

The Project Manager and the Budget Analyst have established levels of signature authority for purchase requisitions written against Project budget codes. The Project is responsible for transmitting this information to the Procurement Department and for monitoring proper conformance to the pre-determined signature levels. A review by various Project personnel may be required, depending on the dollar amount and/or type of purchase requisition or task order.

7.3 Budget Activity and Documentation

Budget activity and change control for the Project is handled in accordance with the approved Project Execution Plan (PEP) and Project Management Plan. The Financial Management System (FMS) in use by Fermilab allows individual cost codes to be established, where necessary. The Budget Analyst has the responsibility for establishing the proper cost codes. The FMS is also used to track and monitor such expenses as charge-backs from other Divisions/Sections, and other Fermilab related costs. At the successful completion of each project phase or WBS task, the Project Manager or designated representative is required to verify that work was performed and completed in accordance with acceptable standards before final payment is authorized by the Business Services Section.

7.4 Verification of Acceptable Quality

At all levels of the Project, QA of purchased material is the responsibility of the requisitioner. Parts and equipment ordered for use must include exact specifications where necessary. This may be achieved by including exact specifications on the purchase requisition and/or by using a Sole Source document. If the materials received do not meet the specifications detailed in the original requisition, then the requisitioner

must notify Purchasing to resolve any discrepancies. If unacceptable parts are discovered through the normal course of use, Purchasing must be informed of the problem. Purchasing will notify the vendor involved and bring the situation to final resolution. Departments are encouraged to document QA non-conformances that may have a negative impact on system performance.

8.0 INSPECTION AND ACCEPTANCE TESTING

8.1 Requirements

Contracted work, purchased equipment, or items produced in Fermilab shops requiring formal inspection and acceptance testing must be identified. When an inspection or acceptance test is to be performed, the inspection techniques to be used will be defined by the testing group. Testing requirements and techniques may be referenced in the resource loaded schedule, a procurement contract, a Memorandum of Understanding, or a Hazard Assessment document. Level 2 Managers are required to identify essential safety items or systems that require formal inspection and testing.

8.2 Documentation

Managers must ensure that the documentation for items that require inspection and acceptance testing is maintained in accordance with the appropriate DOE records retention schedules.

9.0 ASSESSMENT

9.1 Project Management Assessments

The Project Manager has the authority to form an ad hoc review team to investigate quality assurance or quality control non-conformances if the need arises. These formal reviews would be conducted and documented in the Fermilab ES&H Database and Tracking System (ESHTRK).

9.2 Independent Assessments

The QA Program is part of the overall project implementation and is assessed as part of the planned reviews conducted by the Directorate and selected DOE representatives. It is the responsibility of the Project Manager to ensure the information necessary for the review is available and that knowledgeable personnel are available to present the material to the review committees. The Project Manager would also be charged with responding to findings from the independent assessments in accordance with schedules established by the reviewing body and taking action to correct any deficiencies identified by the independent assessments.
